



Asthal Bohar SO 124021
BH000929411IN, IVR No: 69720
01/06/2026 12:57:21, Counter No.
To: DIRECTOR
CHANDIGARH, CHANDIGARH, 160022
From: ASIAN PAINTS
ROHTAK, ROHTAK, 124021
Base Amt: 75.00
To: DIRECTOR
P.Mode: QR
POD:No, www.indiapost.gov.in

Asian Paints Limited
Plot No. 1, Sector - 30B
I.M.T, HSIIDC, Rohtak
Haryana - 124021.
T : (01262) 20 4610
www.asianpaints.com

APL/ROH/EC/25-26/H2

29th May 2026

To,

The Joint Director
Ministry of Environment & Forests (IA Division)
Paryavaran Bhawan, CGO Complex, Lodhi Road
NEW DELHI - 110 003

Dear Sir,

Subject: Environmental clearance for Asian Paints Limited, Rohtak- Half Yearly Compliance Report.

Reference: Letter no. EC25B2601HR5779477N dated 18/09/2025

Please find herewith the enclosed Environment compliance status with respect to the Environmental Clearance given to Asian Paints Limited, Rohtak for the period of 1st October 2025 to 31st March 2026.

Thanking you,

Yours Sincerely,

FOR ASIAN PAINTS LTD.

CC:

i) The Director
Ministry of Environment & Forests
Regional Office (NEZ), Bays No. 24-25, Sector 31-A,
Dakshim Marg,
CHANDIGARH - 160 022

ii) The Member Secretary
HSPCB, Sector-6, C-11, Panchkula, Haryana

iii) The Regional Officer, HSPCB Rohtak Region

Asthal Bohar SO 124021
BH000929411IN, IVR No: 697200926555
01/06/2026 12:57:21, Counter No. 1,
To: MEMBER SECRETARY
PANCHKULA, PANCHKULA, 134100
From: ASIAN PAINTS
ROHTAK, ROHTAK, 124021
Base Amt: 75.00
To: MEMBER SECRETARY
P.Mode: QR
POD:No, www.indiapost.gov.in

Asthal Bohar SO 124021
BH000929411IN, IVR No: 697200926555
01/06/2026 12:57:21, Counter No. 1,
To: JOINT DIRECTOR
DELHI, SOUTH, 110003
From: ASIAN PAINTS
ROHTAK, ROHTAK, 124021
Base Amt: 70.00
To: JOINT DIRECTOR
P.Mode: QR
POD:No, www.indiapost.gov.in

Enclosure: Environmental Clearance conditions compliance status for the period from 1st October 2025 to 31st March 2026 with Annexures.



STATUS OF COMPLIANCE

Descriptive Report on status of compliance to conditions of Environment Clearance (EC)

Project : ASIAN PAINTS LTD.

Project Activity : Integrated Paint Manufacturing

Location : Plot No. 1, Sector 30-B, HSIIDC Industrial Estate, IMT Rohtak,
State-Haryana.

EC Reference : EC25B2601HR5779477N dated 18/09/2025

Period : 1st Oct, 2025 to 31st March 2026

S. No.	EC Conditions	Compliance Status
(A) SPECIFIC CONDITIONS		
1.1	The company shall comply with all the environmental protection measures and safeguards proposed in the documents submitted to the Ministry. All the recommendations made in the EIA/EMP in respect of environmental management and risk mitigation measures relating to the project shall be implemented.	Agreed to Comply All the environmental protection measures and safeguards proposed in the documents submitted to the Ministry shall be complied. All the recommendations made in EIA/EMP in respect of environmental management and risk mitigation measures relating to the project shall be implemented.
1.2	Stack height of 30 m shall be provided to the existing Gas fired boiler (2 x 2 TPH + 1 x 4TPH) as per CPCB /SPCB norms. Stack height of 30 m along with acoustic enclosure shall be provided to each of the existing D.G sets (2 x 1010 KVA; 2 x 2000 KVA), existing GG sets (2 x 2875 KVA) and proposed GG sets (3 x 2875 KVA) as per CPCB/SPCB norms. Dust collector shall be provided to the vent attached to RMG/WPB (processing Block / putty. As proposed, stack height of 30 m shall be provided to the proposed Gas fired boiler (1 x 1 TPH) as per CPCB /SPCB norms.	Complied For existing boilers & DG/GG sets, the stack height 30_m conforms with the extant regulations and the CPCB guidelines. Acoustic enclosure is provided to DG/GG set for controlling noise pollution.  Dust collector provision is available to the vent attached to RMG/WPB (processing Block / putty). For proposed boiler/GG set stack height shall be complied as per norms.

S. No.	EC Conditions	Compliance Status																																													
1.3	Scrubber along with adequate stack height shall be provided to control process emissions viz., VOC generated from the vent attached to paint block and water-based polymer block. The scrubbed water should be sent to ETP for further treatment. Efficiency of scrubbers shall be monitored regularly and maintained properly. At no time, the emission levels shall go beyond the prescribed standards.	Complied Adequate stack height is available for Scrubbers attached to paint and water-based polymer block. Regular maintenance is done to ensure the efficiency of setup.																																													
1.4	Fugitive emissions in the work zone environment, product, raw materials storage area etc. shall be regularly monitored. The emissions shall conform to the limits imposed by SPCB.	Complied Fugitive Emissions in the work zone environment, product, raw materials storage area etc. have been monitored regularly. Monitoring reports attached as Annexure-2.																																													
1.5	Total freshwater requirement from HSIIDC water supply system shall not exceed 1950 m3 /day.	Being Complied. <table><tr><th>Fresh water requireme nt as per EC</th><th>Month</th><th>Actual Water Consumption per month (in m³)</th><th>Working Days in month</th><th>Water Consumption per day (m³)</th></tr><tr><td rowspan="6">1950 m³/day</td><td>Oct'25</td><td>18899</td><td>31</td><td>609.6</td></tr><tr><td>Nov'25</td><td>24058</td><td>30</td><td>801.9</td></tr><tr><td>Dec'25</td><td>20316</td><td>31</td><td>655.4</td></tr><tr><td>Jan'26</td><td>20170</td><td>31</td><td>650.6</td></tr><tr><td>Feb'26</td><td>16419</td><td>28</td><td>586.4</td></tr><tr><td>Mar'26</td><td>20151</td><td>31</td><td>650.0</td></tr><tr><td colspan="2">Average</td><td>20002.17</td><td>30.33</td><td>659.00</td></tr><tr><td colspan="2">Minimum per day</td><td colspan="3">0.00</td></tr><tr><td colspan="2">Maximum per day</td><td colspan="3">1176</td></tr></table> Annexure-4 attached (Conveyance deed with HSIIDC containing water supply details)	Fresh water requireme nt as per EC	Month	Actual Water Consumption per month (in m³)	Working Days in month	Water Consumption per day (m³)	1950 m³/day	Oct'25	18899	31	609.6	Nov'25	24058	30	801.9	Dec'25	20316	31	655.4	Jan'26	20170	31	650.6	Feb'26	16419	28	586.4	Mar'26	20151	31	650.0	Average		20002.17	30.33	659.00	Minimum per day		0.00			Maximum per day		1176		
Fresh water requireme nt as per EC	Month	Actual Water Consumption per month (in m³)	Working Days in month	Water Consumption per day (m³)																																											
1950 m³/day	Oct'25	18899	31	609.6																																											
	Nov'25	24058	30	801.9																																											
	Dec'25	20316	31	655.4																																											
	Jan'26	20170	31	650.6																																											
	Feb'26	16419	28	586.4																																											
	Mar'26	20151	31	650.0																																											
Average		20002.17	30.33	659.00																																											
Minimum per day		0.00																																													
Maximum per day		1176																																													
1.6	NOC from the concerned authority shall be obtained before start of the plant for drawing of the water for the project activities. State Pollution Control Board / Pollution Control Committees shall not issue the Consent to Operate (CTO) under Air (Prevention and Control of Pollution) Act and Water (Prevention and Control of Pollution) Act till the project proponent shall obtain such permission.	Agreed to comply.																																													
1.7	Total Industrial Effluent shall not exceed 178 KLD and shall be treated in ETP (Primary, Secondary and Tertiary) followed by RO, MEE and ATFD. The treated water will be recycled for cooling purpose. Domestic sewage of 50 KLD	Agreed to Comply Quantum of effluent has not exceeded the consented quantity. Industrial effluent and sewage is treated in a ETP cum STP. We are in process of procurement and installation of separate STP and MEE/ATFD.																																													

S. No.	EC Conditions	Compliance Status
	shall be treated in STP and used for horticulture and flushing purposes. The plant shall maintain Zero Liquid Discharge (ZLD) System.	
1.8	The green belt of at least 5 m-10m width shall be developed in an area of 182,666.44 m² or 18.26 ha (34.9%) within plant premises. The industry shall plant 4000 nos. of trees/saplings/plants within premises. Tree saplings selected for the plantation should be of sufficient height, preferably 6-ft shall be planted in greenbelt area. Indigenous species shall only be developed as part of greenbelt and non-indigenous / alien species shall be replaced with native species. No invasive or alien or non-native tree species shall be selected for plantation. PP shall develop at least 20 variety of species as a part of greenbelt. Selection of plant species shall be as per the CPCB guidelines in consultation with the State Forest Department and native species shall be developed. The budget earmarked for the plantation shall be kept in a separate account and should be audited annually. The PP shall annually submit the audited statement along with proof of activities viz. photographs (before & after with geo-location date & time), details of expert agency engaged, details of species planted, number of species planted, survival rate, density of plantation etc. to the Regional Office of MoEF&CC before 1st July of every year for the activities carried out during previous year.	Partially Complied Unit has well developed greenbelt with 34.9% of total plot area. The existing total area of the plot is 129.27 Acres out of which approx. 45.14 acres i.e. 182666.44 m² area is already developed as green belt. Correction proposed for area under greenbelt post expansion at 33% via amendment letter EC/25-26/09 dated 05.11.2025(Annexure-1 attached). Greenbelt development proposed will be completed as per given timelines and report to be submitted before 1st July 2027.
1.9	Plantation of saplings shall be carried out as a part of tree plantation campaign "EK PED MAA ke NAAM" and details of the same to be uploaded in the Meri LiFE portal (https://merilife.nic.in) in respect to this Ministry's OM No. IA3-22/3/2024-IA.III(E-241594) dated 24th July 2024.	Complied ~3000 saplings planted in year 24-25 and 25-26
1.10	Roof top rainwater shall be collected in 2 x 8120 KL. The rainwater collected shall be reused within the plant after filtration as per requirement. Storm water from the open area shall be collected separately and stored in underground RCC storage tank, which shall be recycled/reused within the plant premises.	Not Complied Amendment for correction to 1*8120 KL and aboveground tanks requested via letter no. EC/25-26/09 dated 05.11.2025(Annexure-1 attached)

S. No.	EC Conditions	Compliance Status
1.11	The company shall comply with all the environmental protection measures and safeguards proposed in the documents submitted to the Ministry. All the recommendations made in the EIA/EMP in respect of environmental management and risk mitigation measures relating to the project shall be implemented. The budget proposed under EMP 53.94 Crore (Capital cost) and Rs. 3.20 Crore (Recurring cost)] shall be kept in a separate account and should be audited annually. The PP should submit the annual audited statement along with proof of implementation of activities proposed under EMP duly supported by photographs (before & after with geo-location date & time) and other document as applicable to the Regional Office of MoEF&CC before 1st July of every year for the activities carried out during the previous year.	Not Complied All the environmental protection measures and safeguards proposed in the documents submitted to the Ministry shall be complied. All the recommendations made in the EIA/EMP in respect of environmental management and risk mitigation measures relating to the project shall be implemented. We shall submit the annual audited statement along with proof of implementation of activities proposed under EMP duly supported by photographs (before and after with geo-location date and time) and other documents as applicable to the Regional Office of MoEF and CC before 1st July. Amendment for correction of budget proposed to 2.65 Cr (Capital) requested via letter no. EC/25-26/09 dated 05.11.2025(Annexure-1 attached)
1.12	Continuous online (24x7) monitoring system for stack emissions shall be installed for measurement of flue gas discharge and the pollutants concentration, and the data to be transmitted to the CPCB and SPCB servers. For online continuous monitoring of effluent, the unit shall install web camera with night vision capability and flow meters in the channel/drain carrying effluent within the premises.	Partially Complied Continuous online (24x7) monitoring system for stack emissions is installed for measurement of flue gas discharge and the pollutants concentration, and the data to be transmitted to the CPCB servers. We have submitted requirements to HSPCB and are taking continuous follow-ups for connectivity. Night vision camera to be installed basis applicability.
1.13	No banned Chemicals shall be manufactured by the project proponent. No banned raw materials shall be used in the unit. The project proponent shall adhere to the notifications/guidelines of the Government in this regard.	Complied.
1.14	The project proponent shall comply with the environment norms for paint industry as notified by the Ministry of Environment, Forest and Climate Change, vide GSR 1241 (E), dated 28.12.2018 under the provisions of the Environment (Protection) Rules, 1986.	Agreed to Comply
1.15	All the hazardous waste shall be managed and disposed as per the Hazardous and Other Wastes (Management and Transboundary Movement) Rules, 2016. Hazardous waste such as Distillation Residue and Off Specification Products shall be either sent to common incineration site or send for coprocessing. Solid waste shall be segregated into dry and wet garbage at site in accordance to the Solid Waste	Partially Complied All the hazardous waste managed and disposed as per the Hazardous and Other Wastes (Management and Transboundary Movement) Rules, 2016 and sent for co-processing. Unit has membership of TSDF site namely Gujarat Enviro Protection & Infrastructure (Haryana) Pvt. Ltd. (GEPIL), Faridabad for disposal of hazardous waste (Membership certificate -Annexure-3 attached). Solid waste is segregated into dry and wet garbage at site in accordance to the Solid Waste Management Rules, 2016.

S. No.	EC Conditions	Compliance Status
	Management Rules, 2016. Wet garbage shall be converted into compost and used as manure for greenbelt development.	
1.16	Captive hazardous waste incinerators shall be designed according to the guidelines provided by the Central Pollution Control Board (CPCB). The incinerator shall meet specific performance standards and pollution control norms. Incinerated ash shall be sent to treatment storage disposal facility (TSDF).	Agreed to Comply Incinerator when installed will be as per CPCB guidelines. Co-processing or pre- processing as current mode of disposal.
1.17	A separate Environmental Management Cell (having qualified persons with Environmental Science/Environmental Engineering/specialization in the project area) equipped with full-fledged laboratory facilities shall be set up to carry out the Environmental Management and Monitoring functions by engaging Environment Officials. In addition to this, one safety & health officer as per the qualification given in Factories Act, 1948 shall be engaged within a month of grant of EC. The PP should annually submit the audited statement of amount spent towards the engagement of qualified persons in EMC along with details of person engaged to the Regional Office of MoEF&CC before 1st July of every year for the activities carried out during the previous year.	Complied. A separate Environmental Management Cell (Having qualified persons with experience of the Environmental background) exists. Full-fledged laboratory facilities are available to carry out the Environmental monitoring and analysis functions.
1.18	The PP shall utilize modern technologies for capturing of carbon emitted and shall also develop carbon sink/carbon sequestration resources capable of capturing more than emitted. The implementation report shall be submitted to the IRO, MoEF&CC in this regard.	Partially complied We have increased our efforts towards carbon emission reduction through - Unit has well developed greenbelt with 34.9% of total plot area. - Rooftop solar system of 3676 KWP capacity is installed inside the plant for in-house consumption of energy and a solar power project of 6000 KWP is installed near Siwani (Bhiwani), which supplies energy to the grid(~40% of electricity sourced from Renewable Energy) - Two Diesel Generators were replaced with Gas Generators in 2022-23 which operates using PNG (Piped Natural Gas) - Boiler operates on gas for regular operations
1.19	All necessary precautions shall be taken to avoid accidents and action plan shall be implemented for avoiding accidents. The PP shall implement the onsite/offsite emergency plan/mock drill etc. and mitigation measures as prescribed under the rules and guidelines issued in the Manufacture, Storage and Import of Hazardous Chemicals (MSIHC) Rules, 1989, as	Complied. Unit is complying with all the rules and guidelines under Manufacture, Storage, and Import of Hazardous Chemicals Rules, 1989 as amended in October 1994 and January 2000 and Hazardous Waste (Management and Handling) Rules, 1989, as amended from time to time.


S. No.	EC Conditions	Compliance Status
	amended time to time, and the Chemical Accidents (Emergency Planning, Preparedness and Response) Rules, 1996. The occupier of new as well as expansion projects shall be required to comply with the provisions of the MSHIC Rules, 1989 including notifying their activities or seeking site approval from the concerned authorities, to address operational safety aspects. In doing so, various schedule, particularly Schedule-5 of the said rules may be referred.	
1.20	The volatile organic compounds (VOCs)/Fugitive emissions shall be controlled at 99.97 % with effective chillers/modern technology. Regular monitoring of VOCs shall be carried out	Agreed to Comply Project proponent seeks clarity on the measurement methodology. Existing technology including scrubbers, vapor recovery systems, dust extraction systems for fugitive emissions control exist. Regular monitoring of VOC is carried out in processing areas (Annexure-2 attached).
1.21	The storage of toxic/hazardous raw material shall be bare minimum with respect to quantity and inventory. Quantity and days of storage shall be submitted to the Regional Office of Ministry and SPCB along with the compliance report.	Complied The storage of toxic/hazardous raw material is bare minimum with respect to quantity and inventory. Quantity and days of storage will be submitted to the Regional Office of Ministry and SPCB along with the compliance report. (Annexure – 6)

S. No.	EC Conditions	Compliance Status
1.22	The occupational health centre for surveillance of the worker's health shall be set up. The health data shall be used in deploying the duties of the workers. All workers & employees shall be provided with required safety kits/mask for personal protection	Complied. The occupational health center for surveillance of the worker's health is operational. The health data is used in deploying the duties of the workers. All workers & employees are provided with required safety kits/mask for personal protection. 
1.23	Training shall be imparted to all employees on safety and health aspects for handling chemicals. Safety and visual reality training shall be provided to employees. Action plan for mitigation measures shall be properly implemented based on the safety and risk assessment studies.	Complied. Training is being imparted to all employees on safety and health aspects for handling chemicals. Action plan for mitigation measures is developed and implemented based on the safety and risk assessment studies.
1.24	The unit shall make the arrangement for the protection of possible fire hazards during manufacturing process in material handling. Fire-fighting system shall be as per the norms.	Complied.
1.25	The storm water from the roof top shall be channelized through pipes to the storage tank constructed for harvesting rainwater in the premises and harvested water shall be used for various industrial processes in the unit. No recharge shall be permitted within the premises. Process effluent/ any wastewater shall not be allowed to mix with storm water.	Complied. A separate drain network of storm and roof top is provided in RCC, and entire rainwater is collected into two reservoirs totaling 8120 KL capacity. The setup is regularly cleaned and maintained by PP to avoid any contamination. Collected quantity used in process/utility after suitable water treatment. Also, there is no rainwater recharge permitted in ground at plant premises. 

S. No.	EC Conditions	Compliance Status
1.26	The PP shall undertake waste minimization measures as below (a) Metering and control of quantities of active ingredients to minimize waste; (b) Reuse of by-products from the process as raw materials or as raw material substitutes in other processes. (c) Use of automated filling to minimize spillage. (d) Use of Close Feed system into batch reactors. (e) Venting equipment through vapor recovery system. (f) Use of high pressure-hoses for equipment cleaning to reduce wastewater generation.	Complied - Raw ingredients are added in closed loop manner and is metered for controlled addition in the equipment. - Reactors/Mixers' washing are being collected & reused back in products. - Automated filling system is provided. - All liquid raw materials are charged from storage tank to process vessels in a closed system. - Vapor recovery system is provided for required processing equipment. - High pressure hoses of pressure 100 bar & more are being used for equipment cleaning.
1.27	There shall be adequate space inside the plant premises earmarked for parking of vehicles for raw materials and finished products and no parking to be allowed outside on public places.	Complied.
1.28	Storage of raw materials shall be either in silos or in covered areas to prevent dust pollution and other fugitive emissions. All stockpiles should be constructed over impervious soil and garland drains with catch pits to trap runoff material shall be provided. Chemicals shall be stored in covered sheds and wind breaking walls/curtains shall be provided around biomass storage area to prevent its suspension during high wind speed. All Internal roads shall be paved. The Air Pollution Control System shall be interlocked with process plant/machinery for shutdown in case of operational failure of Air Pollution Control Equipment	Complied. Raw material has been storing in covered areas for dust prevention. Silos used for powder storage. Garland drain is available in tanks area to trap runoff material. 
1.29	PP shall sensitize and create awareness among the people working within the project area as well as its surrounding area on the ban of Single Use Plastic in order to ensure compliance of Notification published by MOEFCC on 12th August, 2021. A report along with photographs on the measures taken shall also be included in the six-monthly compliance report being submitted to concerned authority.	Complied Annexure-9 attached
(B) Standard EC Conditions for (Integrated paint industry)		
1.1	No further expansion or modifications in the plant, other than mentioned in the EIA Notification, 2006 and its amendments, shall be carried out without	Agreed to Comply

S. No.	EC Conditions	Compliance Status
	prior approval of the Ministry of Environment, Forest and Climate Change/SEIAA, as applicable. In case of deviations or alterations in the project proposal from those submitted to this Ministry for clearance, a fresh reference shall be made to the Ministry/SEIAA, as applicable, to assess the adequacy of conditions imposed and to add additional environmental protection measures required, if any	
1.2	The Project proponent shall strictly comply with the rules and guidelines issued under the Manufacture, Storage and Import of Hazardous Chemicals (MSIHC) Rules, 1989, as amended time to time, the Chemical Accidents (Emergency Planning, Preparedness and Response) Rules, 1996, and Hazardous and Other Wastes (Management and Trans-Boundary Movement) Rules, 2016 and other rules notified under various Acts.	Agreed to Comply
1.3	The energy source for lighting purpose shall be preferably LED based, or advanced having preference in energy conservation and environment betterment.	Complied.
1.4	The overall noise levels in and around the plant area shall be kept well within the standards by providing noise control measures including acoustic hoods, silencers, enclosures etc. on all sources of noise generation. The ambient noise levels shall conform to the standards prescribed under the Environment (Protection) Act, 1986 Rules, 1989 viz. 75 dBA (day time) and 70 dBA (night time).	Complied. Noise monitoring reports attached as Annexure-5
1.5	The company shall undertake all relevant measures for improving the socio-economic conditions of the surrounding area. The activities shall be undertaken by involving local villages and administration. The company shall undertake eco-developmental measures including community welfare measures in the project area for the overall improvement of the environment.	Complied. The unit has submitted an Eco-development project plan to HSPCB. In this plan, the company has been focusing on two themes for community welfare, i.e., Health & Hygiene and Water conservation. Eco development plan is attached as Annexure-8
1.6	The company shall earmark sufficient funds towards capital cost and recurring cost per annum to implement the conditions stipulated by the Ministry of Environment, Forest and Climate Change as well as the State Government along with the implementation schedule for all the conditions stipulated herein. The funds so earmarked for environment	Agreed to Comply

S. No.	EC Conditions	Compliance Status
	management/ pollution control measures shall not be diverted for any other purpose.	
1.7	A copy of the clearance letter shall be sent by the project proponent to concerned Panchayat, Zilla Parishad/Municipal Corporation, Urban local Body and the local NGO, if any, from whom suggestions/ representations, if any, were received while processing the proposal.	Agreed to Comply
1.8	The project proponent shall also upload/submit six monthly reports on Parivesh Portal on the status of compliance of the stipulated Environmental Clearance conditions including results of monitored data to the respective Integrated Regional Office of MoEF&CC, the respective Zonal Office of CPCB and SPCB. A copy of Environmental Clearance and six monthly compliance status report shall be posted on the website of the company.	Complied.
1.9	The environmental statement for each financial year ending 31st March in Form-V as is mandated shall be submitted to the concerned State Pollution Control Board as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently, shall also be put on the website of the company along with the status of compliance of environmental clearance conditions and shall also be sent to the respective Integrated Regional Office of MoEF&CC by e-mail.	Complied. FY 24-25 form-V copy sent to Integrated Regional Office via e-mail on 30.09.2025.(Annexure-7 attached)

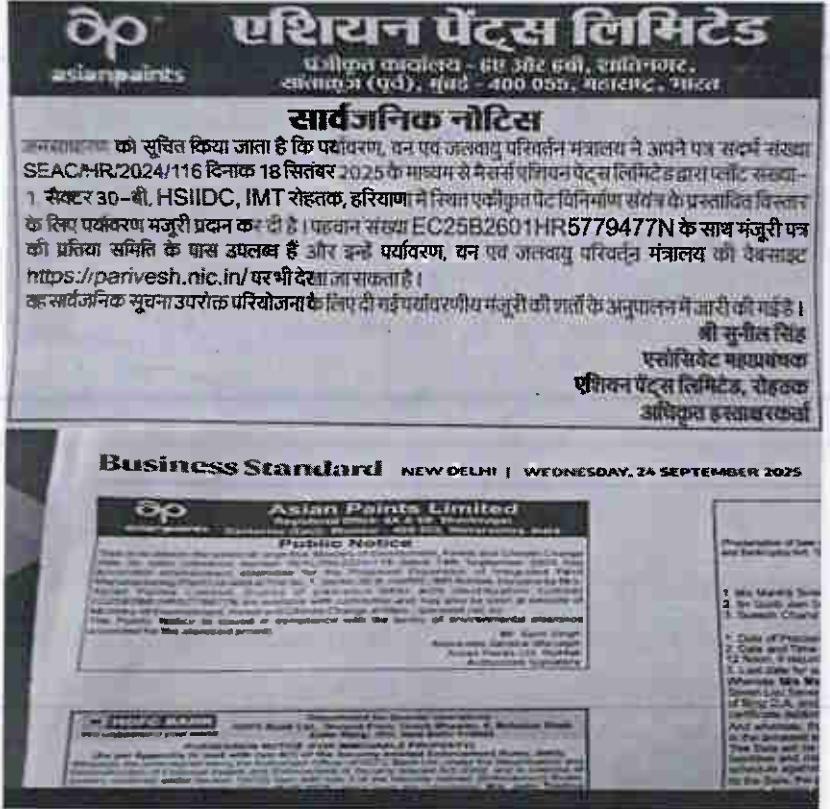S. No.	EC Conditions	Compliance Status
1.10	The project proponent shall inform the public that the project has been accorded environmental clearance by the Ministry and copies of the clearance letter are available with the SPCB/Committee and may also be seen at Website of the Ministry and at https://parivesh.nic.in/ . This shall be advertised within seven days from the date of issue of the clearance letter, at least in two local newspapers that are widely circulated in the region of which one shall be in the vernacular language of the locality concerned and a copy of the same shall be forwarded to the concerned Regional Office of the Ministry	Complied. Public Notice published regarding the same on 24.09.2025 in Dainik Savera (Hindi) and Business Standard (English). PFB the copy of the same- 
1.11	The project authorities shall inform the Regional Office as well as the Ministry, the date of financial closure and final approval of the project by the concerned authorities and the date of start of the project.	Agreed to Comply
1.12	This Environmental clearance is granted subject to final outcome of Hon'ble Supreme Court of India, Hon'ble High Court, Hon'ble NGT and any other Court of Law, if any, as may be applicable to this project.	Agreed to Comply

Handwritten signature

Annexure – A: Copy of Environment Clearance

Annexure – 1: Amendment letter EC/25-26/09 dated 05.11.2025

Annexure – 2: TVOC monitoring reports

Annexure – 3: Hazardous Waste Authorization and Membership Certificate of TSI site

Annexure – 4: Conveyance deed with HSIIDC containing water supply details

Annexure – 5: Workplace noise and ambient noise monitoring reports

Annexure – 6: Details of storage of Toxic/Hazardous Raw material with Quantity

Annexure – 7: Form-V submission mail communication

Annexure – 8: Eco Development plan

Annexure – 9: Single use plastic communications

Annexure -1

Rohtak Sector 1 SO 124001
 ENUS/2131N, IVR No: 10002
 11/11/2025 14:22:41, Counter
 To: JOINT DIRECTOR
 EXPERT APPRAISAL (O), SOUTH, 11
 From: ASIAN PAINTS LTD
 SEC 30 B, ROHTAK, 124001
 Base Amt: 47.00, CGST:4.00, SGST:4.00
 To: JOINT DIRECTOR
 P.Mode: Cash
 POD:No, www.indiapost.gov.in

Asian Paints Limited
 Plot No. 1, Sector - 30B
 I.M.T, HSIIDC, Rohtak
 Haryana - 124021.
 T (01262) 20 4610
 www.asianpaints.com

Ref. No.: EC/25-26/09

Date: 05/11/2025

To,
 Joint Director,
 Expert Appraisal Committee (Industrial Projects-III)
 Ministry of Environment, Forest and Climate Change,
 Indira Paryavaran Bhavan, Jorbagh Road,
 New Delhi-110003

Subject: Amendment Request for Environment Clearance conditions regarding proposed expansion of Integrated Paint Manufacturing Plant Located at Plot No-1, Sector 30-B, HSIIDC, IMT Rohtak, State Haryana by Asian Paints Limited

Proposal No.: IA/HR/IND3/526333/2025

MoEFCC File No.: SEAC/HR/2024/116

Ref.: 1. Environment Clearance ID no- EC25B2601HR5779477N

2. MoM ID- EC/MOM/EAC/274949/8/2025

Dear Sir,

With reference to the Environmental Clearance received on 18th September with identification number EC25B2601HR5779477N for **proposed expansion of Integrated Paint Manufacturing Plant at Located at Plot No-1, Sector 30-B, HSIIDC, IMT Rohtak, State Haryana by Asian Paints Limited**, we hereby request you to consider following amendments in the conditions of EC recommendations and final EC letter:

Condition No.	Description	Amendment Sought	Justification / Explanation
(vii)	Total Industrial Effluent shall not exceed 178 KLD and shall be treated in ETP (Primary, Secondary and Tertiary) followed by RO, MEE and ATFD. The treated water will be recycled for cooling purpose. Domestic sewage of 50 KLD shall be treated in STP and used for horticulture and flushing purposes. The plant shall maintain Zero Liquid Discharge (ZLD) System.	Total Industrial Effluent shall not exceed 178 KLD and shall be treated in ETP (Primary, Secondary and Tertiary) followed by RO, MEE and ATFD. Domestic sewage of 50 KLD shall be treated in ETP. The treated water will be recycled for cooling purposes. The plant shall maintain Zero Liquid Discharge (ZLD) System.	The present scheme of treatment in ETP is that industrial effluent is collected in Equalization Tank and further undergoes primary treatment with coagulation and flocculation process. Overflow of primary clarifier is taken to an aeration tank where sewage waters are mixed in a biological treatment system. The domestic sewage addition in Aeration Tank is essential for providing continuous microbial load to the existing biomass to absorb shock loading condition.

Registered Office : Asian Paints Limited, 6A & 6B, Shantinagar Santacruz (East) Mumbai - 400 055. tel : (022) 6218 1000 Fax : (022) 6218 1111

Condition No.	Description	Amendment Sought	Justification / Explanation
			This is in line with the presentation made and we request you consider the common set-up for further consideration. Refer 3.1.4 Point 1
(vi)	The green belt of at least 5 m-10m width shall be developed in an area of 182,666.44 m ² or 18.26 ha (34.9%) within plant premises. The industry shall plant 4000 nos. of trees/saplings/plants within premises. Tree saplings selected for the plantation should be of sufficient height, preferably 6-ft shall be planted in greenbelt area. Indigenous species shall only be developed as part of greenbelt and non-indigenous / alien species shall be replaced with native species. No invasive or alien or non-native tree species shall be selected for plantation. PP shall develop at least 20 variety of species as a part of greenbelt. Selection of plant species shall be as per the CPCB guidelines in consultation with the State Forest Department and native species shall be developed. The budget earmarked for the plantation shall be kept in a separate account and should be audited annually. The PP shall annually submit the audited statement along with proof of activities viz. photographs (before & after with geo-location date & time), details of expert agency engaged, details of species planted, number of species planted, survival rate, density of plantation etc. to the Regional Office of MoEF&CC before 1st July of every year for the activities carried out during previous year.	The green belt of at least 5 m-10m width shall be developed in an area of 172,666.44 m ² or 17.26 ha (33%) within plant premises. The industry shall plant 4000 nos. of trees/saplings/plants within premises. Tree saplings selected for the plantation should be of sufficient height, preferably 6-ft shall be planted in greenbelt area. Indigenous species shall only be developed as part of greenbelt and non-indigenous / alien species shall be replaced with native species. No invasive or alien or non-native tree species shall be selected for plantation. PP shall develop at least 20 variety of species as a part of greenbelt. Selection of plant species shall be as per the CPCB guidelines in consultation with the State Forest Department and native species shall be developed. The budget earmarked for the plantation shall be kept in a separate account and should be audited annually. The PP shall annually submit the audited statement along with proof of activities viz. photographs (before & after with geo-location date & time), details of expert agency engaged, details of species planted, number of species planted, survival rate, density of plantation etc. to the Regional Office of MoEF&CC before 1st July of every year for the activities carried out during previous year.	Greenbelt area after proposed expansion will be 33% i.e. 17.26 ha as mentioned in Table 2.4 EIA area breakup details (Annexure 1). Industry shall plant 4000 saplings in the proposed area as per the greenbelt development plan and will at least maintain 5-10 m belt. Therefore, we request you to reconsider the conditions as stated and revise the figures.
(x)	Roof top rain water shall be collected in 2 x 8120 KL. The rain water collected shall be reused within the plant after filtration as per requirement. Storm water from the open area shall be collected separately and stored in underground RCC storage	Rainwater shall be separately collected in two reservoirs leading to total capacity of 8120 KL. The rainwater collected shall be reused within the plant after filtration as per requirement. Storm water and roof water shall be collected separately and stored in aboveground RCC storage	Requesting the change required from 2*8120 to two reservoirs to a total capacity of 8120 KL separately for storm water and roof water including above ground built.

Registered Office : Asian Paints Limited, 6A & 6B, Shantinagar Santacruz (East) Mumbai - 400 055. tel : (022) 6218 1000 fax : (022) 6218 1111

Condition No.	Description	Amendment Sought	Justification / Explanation
	tank, which shall be recycled/reused within the plant premises.	tank, which shall be recycled/reused within the plant premises.	
(xi)	The company shall comply with all the environmental protection measures and safeguards proposed in the documents submitted to the Ministry. All the recommendations made in the EIA/EMP in respect of environmental management, and risk mitigation measures relating to the project shall be implemented. The budget proposed under EMP 53.94 Crore (Capital cost) and Rs. 3.20 Crore (Recurring cost)) shall be kept in a separate account and should be audited annually. The PP should submit the annual audited statement along with proof of implementation of activities proposed under EMP duly supported by photographs (before & after with geo-location date & time) and other document as applicable to the Regional Office of MoEF&CC before 1st July of every year for the activities carried out during the	The company shall comply with all the environmental protection measures and safeguards proposed in the documents submitted to the Ministry. All the recommendations made in the EIA/EMP in respect of environmental management, and risk mitigation measures relating to the project shall be implemented. The budget proposed under EMP 2.65 Crore (Capital cost) and Rs. 3.20 Crore (Recurring cost)) shall be kept in a separate account and should be audited annually. The PP should submit the annual audited statement along with proof of implementation of activities proposed under EMP duly supported by photographs (before & after with geo-location date & time) and other document as applicable to the Regional Office of MoEF&CC before 1st July of every year for the activities carried out during the	Please note that 53.94 Crore is incurred expense/CAPEX and the proposed amount is 2.65 Cr as mentioned in EIA EMP (Annexure 2)

Hence, we request you to kindly reconsider the aforesaid amendments and make the necessary changes in the Environment Clearance.

Thank you

Yours Sincerely

For, Asian Paints Limited



Authorized Signatory

Registered Office : Asian Paints Limited, 6A & 6B, Shantinagar Santacruz (East) Mumbai - 400 055. tel : (022) 6218 1000 fax : (022) 6218 1111

Annexure 1-

Table 2-4: Area Break up at Site

S. No.	Title	Area (m ²)			% of the Total Area
		Existing	Proposed Expansion	Total After Expansion	
1	Processing Area	23,114.72	11,811.10	34,925.82	6.7%
2	Storage Area				0.0%
a	Hazardous Chemical	11592.03	-	11592.03	2.2%
b	Other Non-Hazardous Chemicals	13,066.14	-	13,066.14	2.5%
c	Hazardous Waste	970.95	-	970.95	0.2%
d	Water Storage	3,818.13	-	3,818.13	0.7%
e	Fuel, Solvent and other liquid chemical storage	10,281.51	1,028.15	11,309.66	2.2%
3	Wastewater treatment plant (ETP)	2,247.91	-	2,247.91	0.4%
4	Boiler	4,296.20	859.24	5,155.44	1.0%
5	Utilities	392.29	-	392.29	0.1%
6	DG & LT Room	1,943.19	2,914.79	4,857.98	0.9%
7	Roads	101,691.80	-	1,01,691.80	19.4%
8	Administrative Building, Security Cabin	6,491.00	-	6,491.00	1.2%
9	Greenbelt Area	182,666.44	-10,011.10	1,72,655.34	33.0%
10	Other/ Open area	160,625.69	-6602.18	1,54,023.51	29.4%

Annexure 2-

Table 10-16: Expenditure on Environmental Matters

S. No.	Need	Approximate Capital cost (INR, Lakhs)	Proposed CAPEX (INR, Lakhs)	Approximate recurring cost per annum (INR, lakhs)	Basis for cost estimates
1.	Air pollution control	Inverter: 120 DG: 528 Accessories: 130 Reverse Jet Filter: 600 Dust collector: 86 Scrubber System and Accessories: 100	Dust Collector, R/F, Scrubber etc: 100	Air Monitoring: 1.3 APC: 10	Capital Cost: include cost of proposed stack, ESP, Multi cyclone, bag filter, Tail gas absorber Recurring costs: Manpower, Monitoring, operation of APCM
2.	Water pollution control	Effluent treatment plant construction: 900 RO: 200 MEE: 53	Refurbishing: 50	Operations: 25 Effluent Testings: 1.48 OCCMS: 1.2	Capital Cost: include cost of Proposed ETP including RO and MEE Augmentation cost,

KALAM ENVIRONMENTAL CONSULTANTS | FEBRUARY 2025

341

ASIAN PAINTS LTD. PROPOSED EXPANSION OF INTEGRATED PAINT MANUFACTURING PLANT AT HSJDC, DMT BONTAL, MARIYANA ENVIRONMENTAL MANAGEMENT PLAN

S. No.	Need	Approximate Capital cost (INR, Lakhs)	Proposed CAPEX (INR, Lakhs)	Approximate recurring cost per annum (INR, lakhs)	Basis for cost estimates
		Wash water reuse projects and Scheme: 100		Calibration, Manpower Cost: 40	Recurring cost: Manpower, Chemical, Running cost, Monitoring cost
3.	Noise pollution	OG Acoustic Enclosure cost: 9.41	Nil	Noise Monitoring: 3	Capital Cost: Acoustic Enclosure cost, Recurring Cost: Cost of noise monitoring
4.	Solid and hazardous waste management	Membership fees: 0.05, Storage: 150	Nil	Cost of Disposal: 75	Capital Cost: 1) Membership fee of HSSE Site and CHAW/Channarayana, 2) Cost of Membership for 1% ash disposal, 3) storage of hazardous waste, Recurring cost: Transportation cost, Disposal Cost
5.	Environment monitoring and management	As and when required	As and when required	As and when required	The recurring cost would be incurred on hiring of consultants and payment of various statutory fees to regulatory agencies.
6.	Green belt	Landscape Irrigation System: 24, Landscaping, Trees etc: 2100 (on basis cost 100rs/2)	Proposed: 20	Recurring plantation: 4, Maintenance cost: 30	Capital Cost: Proposed Greenbelt Development Cost, Recurring Cost: Greenbelt Maintenance cost
7.	Occupational Health & Safety	OHC Infra: 25, O2 Cylinder: 1.5, BP Instruments, First Aid and other devices: 1, Ambulance: 19, AED MACHINE: 0.32, Fire Safety Equipment's: 5	Nil	Recurring cost: 81 Eg calibration: 0.3 Medical health Checkup: 1.8	Capital Cost: Installation of OHC Building, examination table, O2 Cylinder, BP Instruments, First Aid Box, Ambulance etc. For safety installation of PPEs, Fire Extinguisher, Fire Hydrant system (Pressure Boost up pump, Electric Operated pump & Diesel Operated Pumps, Lines, Hydrant monitor, sprinkler system, fire water tank) Detectors, Sensors, etc. Recurring Cost (per annum): Cost of Doctor & Nurses, Maintenance of medical equipment, Maintenance of safety measures
8.	CER Cost	250	95	19	0.75% of Total project cost will be utilized under health such as Water conservation & other ecological conservation projects
Total		5394.28	265	320.98	

Annexure -2

Jan-26

Work Zone- VOC-TWA

**Industrial Environmental Sampling, Monitoring,
Analysis & Reporting Data**

of

ASIAN PAINTS LIMITED.

Plot No. – 01, IMT, Kheri Sadh,

Rohtak (Haryana) – 24001 India

By

ENVIROINTERNATIONAL

Plot No 138-139, UK-II, Eco Tech-III,



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India, recognised as refn LB-2021/7/99/IIlab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP, Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285, UPPCB-HD/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. – 01, IMT, Kheri Sadh, Rohtak (Haryana) – 124001 India.		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT , GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/WZ-13		Sample Collection Date: 15/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	POLYMER Hind FLOOR NEW BLOCK
Sampling Code	--	--	WZ - 13
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	290
Acetone	mg/m ³	<1780	230
Ammonia	mg/m ³	<18	08
n-Butyl acetate	mg/m ³	<710	93
n-Butyl alcohol	mg/m ³	<150	81
Ethyl acetate	mg/m ³	<1400	98
Ethyl alcohol	mg/m ³	<1900	61
Formaldehyde	mg/m ³	<1.5	0.7
Isobutyl alcohol	mg/m ³	<150	42
Manganese dust and compounds (as Mn)	mg/m ³	<05	BDL
Phosphoric Acid	mg/m ³	<01	BDL
Pyridine	mg/m ³	<15	13
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	64
Phthalic Anhydride	mg/m ³	<01	BDL
Toluene	mg/m ³	<375	51
2 - Ethylhexanoic acid (2-EHA)	mg/m ³	<376	92
Butanol	mg/m ³	<152	54
Butyl Cellosolve	mg/m ³	<123	67
Ethyl Cellosolve Acetate	mg/m ³	<55	33
Mineral Turpentine Oil (MTO)	mg/m ³	<560	236
Acetic Acid	mg/m ³	<25	BDL
2 - Butanone (Methyl ethyl Ketone – MEK)	mg/m ³	<500	BDL
sec/tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	—	BDL
Nitric Acid	mg/m ³	<05	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	—	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<01	BDL

N. B. A. Methods Based on NIOSH, OSHA & CPCB. B. Standard as per Fact Act 1948. C. BDL :- <0.05 mg/m³

Sampling Done By Mr Shiv Singh & Mr Purshotam Singh.

Checked

R.P. Marwah

EIL/Lab In-Charge

Dr. Vipul Kumar

Greater Noida

N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
 : 9810098664, 9810725666, 9910233668
 : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC-17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India, recognised as refn LB-2021/7/99/lab-HQ-CPCB-HQ/Pvt/2371, Environmental Laboratory RV Enviro International LLP, Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285, UPPCB-HQ/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. – 01, IMT, Kheri Sadh, Rohtak (Haryana) – 124001 India.		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT , GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/WZ-2		Sample Collection Date: 14/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	WPB- GROUND FLOOR-OLD BLOCK
Sampling Code	--	--	WZ – 02
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	28.9
Acetone	mg/m ³	<1780	140
Ammonia	mg/m ³	<18	06
n-Butyl acetate	mg/m ³	<710	49
n-Butyl alcohol	mg/m ³	<150	18
Ethyl acetate	mg/m ³	<1400	31
Ethyl alcohol	mg/m ³	<1900	49
Formaldehyde	mg/m ³	<1.5	0.9
Isobutyl alcohol	mg/m ³	<150	08
Manganese dust and compounds (as Mn)	mg/m ³	<0.5	BDL
Phosphoric Acid	mg/m ³	<0.1	BDL
Pyridine	mg/m ³	<15	BDL
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	81
Phthalic Anhydride	mg/m ³	<0.1	BDL
Toluene	mg/m ³	<375	46
2 – Ethylhexanoic acid (2-EHA)	mg/m ³	<376	39
Butanol	mg/m ³	<152	08
Butyl Cellosolve	mg/m ³	<123	22
Ethyl Cellosolve Acetate	mg/m ³	<55	19
Mineral Turpentine Oil (MTO)	mg/m ³	<560	107
Acetic Acid	mg/m ³	<25	BDL
2 – Butanone (Methyl ethyl Ketone – MEK)	mg/m ³	<590	BDL
sec/tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	–	BDL
Nitric Acid	mg/m ³	<0.5	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	–	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<0.1	BDL

N. B. A. Methods Based on NIOSH, OSHA & CPCB. B. Standard as per Fact Act 1948. C. BDL : <0.05 mg/m³
 Sampling Done By Mr Shiv Singh & Mr Purshotam Singh.

Checked
 R.P. Mahwah

EIL Lab-In-Charge
 Dr. Vipul Kumar
 Greater Noida

N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
 ☎ : 9810098664, 9810725666, 9910233668
 ✉ : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC 17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India, recognised as refn LB-2021/7/99/IIlab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP, Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285, UPPCB-HO/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. – 01, IMT, Kheri Sadh, Rohtak (Haryana) – 124001 India..		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT , GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/VZ-3		Sample Collection Date: 14/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	WPB GROUND FLOOR NEW BLOCK
Sampling Code	--	--	WZ – 03
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	289
Acetone	mg/m ³	<1780	164
Ammonia	mg/m ³	<18	14
n-Butyl acetate	mg/m ³	<710	70
n-Butyl alcohol	mg/m ³	<150	11
Ethyl acetate	mg/m ³	<1400	89
Ethyl alcohol	mg/m ³	<1900	91
Formaldehyde	mg/m ³	<1.5	0.9
Isobutyl alcohol	mg/m ³	<150	09
Manganese dust and compounds (as Mn)	mg/m ³	<05	BDL
Phosphoric Acid	mg/m ³	<01	BDL
Pyridine	mg/m ³	<15	BDL
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	53
Phthalic Anhydride	mg/m ³	<01	BDL
Toluene	mg/m ³	<375	111
2 – Ethylhexanoic acid (2-EHA)	mg/m ³	<376	41
Butanol	mg/m ³	<152	09
Butyl Cellosolve	mg/m ³	<123	10
Ethyl Cellosolve Acetate	mg/m ³	<55	06
Mineral Turpentine Oil (MTO)	mg/m ³	<560	125
Acetic Acid	mg/m ³	<25	BDL
2 – Butanone (Methyl ethyl Ketone – MEK)	mg/m ³	<590	BDL
sec./tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	--	BDL
Nitric Acid	mg/m ³	<05	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	--	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<01	BDL

N. B. A. Methods Based on NIOSH, OSHA & CPCB. B. Standard as per Fact Act 1948. C. BDL > <0.05 mg/m³
 Sampling Done By Mr Shiv Singh & Mr Purshotam Singh.

Checked
 R.P. Marwah



N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
 9810098664, 9810725666, 9910233668
 : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO 17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India, recognised as rin LB-2021/7/99/IIab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP, Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285, UPPCB-HO/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO :

M/s ASIAN PAINTS LIMITED

Plot No. - 01, IMT, Kheri Sadh,

Rohtak (Haryana) - 124001 India.

Sample Details : VOC-TWA

Sample Reference: EIL/APL-R/01/26/VZ-18

SUBJECT : VOC-TWA

METHODS : Based on NIOSH, OSHA

INSTRUMENTS: Handy Sampler, CT, GC, UV etc.

Sample Collection Date: 14/01/26

Sample Reporting Date: 30/01/26

ANALYSIS REPORT

SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	LQC
Sampling Code	--	--	WZ-18
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	290
Acetone	mg/m ³	<1780	389
Ammonia	mg/m ³	<18	13
n-Butyl acetate	mg/m ³	<710	297
n-Butyl alcohol	mg/m ³	<150	80
Ethyl acetate	mg/m ³	<1400	201
Ethyl alcohol	mg/m ³	<1900	169
Formaldehyde	mg/m ³	<1.5	1.0
Isobutyl alcohol	mg/m ³	<150	114
Manganese dust and compounds (as Mn)	mg/m ³	<0.5	BDL
Phosphoric Acid	mg/m ³	<0.1	BDL
Pyridine	mg/m ³	<15	11
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	192
Phthalic Anhydride	mg/m ³	<0.1	BDL
Toluene	mg/m ³	<378	151
2 - Ethylhexanoic acid (2-EHA)	mg/m ³	<376	96
Butanol	mg/m ³	<152	70
Butyl Cellosolve	mg/m ³	<123	99
Ethyl Cellosolve Acetate	mg/m ³	<55	43
Mineral Turpentine Oil (MTO)	mg/m ³	<560	291
Acetic Acid	mg/m ³	<25	BDL
2 - Butanone (Methyl ethyl Ketone - MEK)	mg/m ³	<590	BDL
sec./tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	--	BDL
Nitric Acid	mg/m ³	<0.5	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	--	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<0.1	BDL

N. B. A. Methods Based on NIOSH, OSHA & CPCB.

B. Standard as per Fact Act 1948.

C. BDL > <0.05 mg/m³

Sampling Done By Mr Shiv Singh & Mr Purnotom Singh.

Checked

R.P. Marwah

EIL/Lab-In-Charge

Dr. Vipul Kumar

Greater
Noida

N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306

☎ : 9810098664, 9810725666, 9910233668

✉ : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC 17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India, recognised as refn LB-2021/7/99/IIab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP, Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285, IUPCB-HO/600/CC/89/2009-10/2023, ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018

TEST REPORT


ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. - 01, IMT, Kheri Sadh, Rohtak (Haryana) - 124001 India.		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT , GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/WZ-25		Sample Collection Date: 17/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	ETP Chemical Preparation Area
Sampling Code	--	--	WZ - 25
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	293
Acetone	mg/m ³	<1780	183
Ammonia	mg/m ³	<18	11
n-Butyl acetate	mg/m ³	<718	97
n-Butyl alcohol	mg/m ³	<150	27
Ethyl acetate	mg/m ³	<1400	31
Ethyl alcohol	mg/m ³	<1900	136
Formaldehyde	mg/m ³	<1.5	0.9
Isobutyl alcohol	mg/m ³	<150	148
Manganese dust and compounds (as Mn)	mg/m ³	<05	BDL
Phosphoric Acid	mg/m ³	<01	BDL
Pyridine	mg/m ³	<15	10
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	152
Phthalic Anhydride	mg/m ³	<01	BDL
Toluene	mg/m ³	<375	95
2 - Ethylhexanoic acid (2-EHA)	mg/m ³	<376	110
Butanol	mg/m ³	<152	37
Butyl Cellosolve	mg/m ³	<123	51
Ethyl Cellosolve Acetate	mg/m ³	<55	40
Mineral Turpentine Oil (MTO)	mg/m ³	<560	202
Acetic Acid	mg/m ³	<25	BDL
2 - Butanone (Methyl ethyl Ketone - MEK)	mg/m ³	<590	BDL
sec/tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Flouride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	--	BDL
Nitric Acid	mg/m ³	<05	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	--	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<01	BDL

N. B. A. Methods Based on NIOSH, OSHA & CPCB. B. Standard as per Fact Act 1948. C. BDL < 0.05 mg/m³

Sampling Done By Mr Shiv Singh & Mr Purshotam Singh.

Checked

R.P. Mathias



N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
 : 9810098664, 9810725666, 9910233668
 : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC-17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India,
recognised as refn LB-2021/7/99/IIab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP,
Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B Nagar-UP 201306, NABL TC-15285,
UPPCB-HO/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2015

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. – 01, IMT, Kheri Sadh, Rohtak (Haryana) - 124001 India.		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT , GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/WZ-24		Sample Collection Date: 17/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	BCY
Sampling Code	--	--	WZ- 24
Sampling Duration	--	--	400 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	293
Acetone	mg/m ³	<1780	306
Ammonia	mg/m ³	<18	11
n-Butyl acetate	mg/m ³	<710	132
n-Butyl alcohol	mg/m ³	<150	125
Ethyl acetate	mg/m ³	<1400	159
Ethyl alcohol	mg/m ³	<1900	194
Formaldehyde	mg/m ³	<1.5	0.8
Isobutyl alcohol	mg/m ³	<150	69
Manganese dust and compounds (as Mn)	mg/m ³	<05	BDL
Phosphoric Acid	mg/m ³	<01	BDL
Pyridine	mg/m ³	<15	11
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	157
Phthalic Anhydride	mg/m ³	<01	BDL
Toluene	mg/m ³	<375	140
2 - Ethylhexanoic acid (2-EHA)	mg/m ³	<376	166
Butanol	mg/m ³	<152	151
Butyl Cellosolve	mg/m ³	<123	94
Ethyl Cellosolve Acetate	mg/m ³	<55	47
Mineral Turpentine Oil (MTO)	mg/m ³	<560	192
Acetic Acid	mg/m ³	<25	BDL
2 - Butanone (Methyl ethyl Ketone – MEK)	mg/m ³	<590	BDL
sec./tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	—	BDL
Nitric Acid	mg/m ³	<05	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	—	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<01	BDL

N. B. A. Methods Based on NIOSH, OSHA & CPCB. B. Standard as per Fact Act 1948.

Sampling Done By Mr Shiv Singh & Mr Purshotam Singh.

Checked

R.P. Narwah

C. BDL <0.05 mg/m³

BDL Lab In-Charge



N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
 ☎ : 9810098664, 9810725666, 9910233668
 ✉ : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



NOV/2021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India, recognised as refn LB-2021/7/99/lab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP, Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285, UPPCB-HO/500/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. – 01, IMT, Kheri Sadh, Rohtak (Haryana) – 124001 India.		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT , GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/WZ-23		Sample Collection Date: 17/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	MTF
Sampling Code	--	--	WZ – 23
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	293
Acetone	mg/m ³	<1780	179
Ammonia	mg/m ³	<18	11
n-Butyl acetate	mg/m ³	<710	137
n-Butyl alcohol	mg/m ³	<150	96
Ethyl acetate	mg/m ³	<1400	90
Ethyl alcohol	mg/m ³	<1900	83
Formaldehyde	mg/m ³	<1.5	0.7
Isobutyl alcohol	mg/m ³	<150	97
Manganese dust and compounds (as Mn)	mg/m ³	<05	BDL
Phosphoric Acid	mg/m ³	<01	BDL
Pyridine	mg/m ³	<15	06
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	142
Phthalic Anhydride	mg/m ³	<01	BDL
Toluene	mg/m ³	<375	177
2 – Ethylhexanoic acid (2-EHA)	mg/m ³	<376	130
Butanol	mg/m ³	<152	122
Butyl Cellosolve	mg/m ³	<123	57
Ethyl Cellosolve Acetate	mg/m ³	<55	31
Mineral Turpentine Oil (MTO)	mg/m ³	<560	153
Acetic Acid	mg/m ³	<25	BDL
2 – Butanone (Methyl ethyl Ketone – MEK)	mg/m ³	<590	BDL
sec/tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	—	BDL
Nitric Acid	mg/m ³	<05	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	—	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<01	BDL

N.B. A. Methods Based on NIOSH, OSHA & GPCB. B. Standard as per Fact Act 1948. C. BDL :- <0.05 mg/m³

Sampling Done By Mr Shriv Singh & Mr Purshotam Singh.

Checked

R.P. Mahwah



N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
 : 9810098664, 9810725666, 9910233668
 : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC-17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India, recognised as refn LB-2021/7/99/IIab-HO-CPCB-HO/PvU/2371, Environmental Laboratory RV Enviro International LLP, Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285, UPPCB-HO/690/CC/89/2009-10/2023, ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. - 01, IMT, Kheri Sadh, Rohtak (Haryana) - 124001 India. Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/WZ-29		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT, GC, UV etc. Sample Collection Date: 17/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	Scrap Yard
Sampling Code	--	--	WZ - 29
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	293
Acetone	mg/m ³	<1780	120
Ammonia	mg/m ³	<18	03
n-Butyl acetate	mg/m ³	<710	30
n-Butyl alcohol	mg/m ³	<150	21
Ethyl acetate	mg/m ³	<1400	58
Ethyl alcohol	mg/m ³	<1900	61
Formaldehyde	mg/m ³	<1.5	0.2
Isobutyl alcohol	mg/m ³	<150	40
Manganese dust and compounds (as Mn)	mg/m ³	<05	BDL
Phosphoric Acid	mg/m ³	<01	BDL
Pyridine	mg/m ³	<15	04
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	40
Phthalic Anhydride	mg/m ³	<01	BDL
Toluene	mg/m ³	<375	52
2 - Ethylhexanoic acid (2-EHA)	mg/m ³	<376	21
Butanol	mg/m ³	<152	27
Butyl Cellosolve	mg/m ³	<123	32
Ethyl Cellosolve Acetate	mg/m ³	<55	11
Mineral Turpentine Oil (MTO)	mg/m ³	<560	155
Acetic Acid	mg/m ³	<25	BDL
2 - Butanone (Methyl ethyl Ketone - MEK)	mg/m ³	<590	BDL
sec/tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	--	BDL
Nitric Acid	mg/m ³	<05	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	--	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<01	BDL

NN. B. A. Methods Based on NIOSH, OSHA & CPCB.
 Sampling Done By Mr Shiv Singh & Mr Purshotam Singh.

B. Standard as per Fact Act 1948.

C. BDL > <0.05 mg/m³

Checked
 R.P. Marwah

EN/Lab-In-Charge
 Dr. Vinod Kumar
 Director
 Noida

N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
 : 9810098664, 9810725666, 9910233668
 : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC 17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India, recognised as refn LB-2021/7/99/IIlab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP, Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285, UPPCB-HO/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. - 01, IMT, Kheri Sadh, Rohtak (Haryana) - 124001 India..		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT , GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/WZ-14		Sample Collection Date: 16/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	QUALITY ASSURANCE QA CHMICAL ROOM
Sampling Code	--	--	WZ - 14
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	292
Acetone	mg/m ³	<1780	276
Ammonia	mg/m ³	<18	13
n-Butyl acetate	mg/m ³	<710	99
n-Butyl alcohol	mg/m ³	<150	63
Ethyl acetate	mg/m ³	<1400	126
Ethyl alcohol	mg/m ³	<1900	80
Formaldehyde	mg/m ³	<1.5	1.1
Isobutyl alcohol	mg/m ³	<150	57
Manganese dust and compounds (as Mn)	mg/m ³	<85	BDL
Phosphoric Acid	mg/m ³	<01	BDL
Pyridine	mg/m ³	<15	08
Methyl isobutyl ketone (MIBK)	mg/m ³	<285	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	67
Phthalic Anhydride	mg/m ³	<01	BDL
Toluene	mg/m ³	<375	91
2 - Ethylhexanoic acid (2-EHA)	mg/m ³	<376	67
Butanol	mg/m ³	<152	44
Butyl Cellosolve	mg/m ³	<123	106
Ethyl Cellosolve Acetate	mg/m ³	<55	37
Mineral Turpentine Oil (MTO)	mg/m ³	<560	262
Acetic Acid	mg/m ³	<25	BDL
2 - Butanone (Methyl ethyl Ketone - MEK)	mg/m ³	<390	BDL
sec/tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	--	BDL
Nitric Acid	mg/m ³	<05	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	--	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<01	BDL

N. B. A. Methods Based on NIOSH, OSHA & CPCB.

B. Standard as per Fact Act 1948.

C. BDL :- <0.05 mg/m³

Sampling Done By Mr Shiv Singh & Mr Purshotam Singh.

Checked

R.P. Marwan

EIL/Lab-In-Charge

Dr Vipul Kumar

Greater Noida

N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
 : 9810098664, 9810725666, 9910233668
 : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC 17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India,
recognised as ref LB-2021/7/99/IIab-HQ-CPCB-HQ/Pvt/2371, Environmental Laboratory RV Enviro International LLP,
Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285,
UPPCB-HQ/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. – 01, IMT, Kheri Sadh, Rohtak (Haryana) – 124001 India..		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT , GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/VZ-16		Sample Collection Date: 16/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	QUALITY ASSURANCE QA HPLC ROOM
Sampling Code	--	--	WZ- 16
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	292
Acetone	mg/m ³	<1780	204
Ammonia	mg/m ³	<18	09
n-Butyl acetate	mg/m ³	<710	91
n-Butyl alcohol	mg/m ³	<150	78
Ethyl acetate	mg/m ³	<1400	37
Ethyl alcohol	mg/m ³	<1900	81
Formaldehyde	mg/m ³	<1.5	0.7
Isobutyl alcohol	mg/m ³	<150	78
Manganese dust and compounds (as Mn)	mg/m ³	<0.5	BDL
Phosphoric Acid	mg/m ³	<0.1	BDL
Pyridine	mg/m ³	<15	11
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	91
Phthalic Anhydride	mg/m ³	<0.1	BDL
Toluene	mg/m ³	<375	103
2 - Ethylhexanoic acid (2-EHA)	mg/m ³	<376	95
Butanol	mg/m ³	<152	14
Butyl Cellosolve	mg/m ³	<123	77
Ethyl Cellosolve Acetate	mg/m ³	<55	41
Mineral Turpentine Oil (MTO)	mg/m ³	<560	195
Acetic Acid	mg/m ³	<25	BDL
2 - Butanone (Methyl ethyl Ketone - MEK)	mg/m ³	<590	BDL
sec./tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	--	BDL
Nitric Acid	mg/m ³	<0.5	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	--	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<0.1	BDL

N.B. A. Methods Based on NIOSH, OSHA & GPCB.
Sampling Done By Mr Shlv Singh & Mr Purshotam Singh.

B. Standard as per Fact Act 1948.

C. BDL :- <0.05 mg/m³

Checked

R.P. Mahwah

EIL/Lab-In-Charge

Dr. Vipul Kumar

Greater Noida

N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306

☎ : 9810098664, 9810725666, 9910233668

✉ : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



1EC-17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India,
recognised as rin LB-2021/7/99/IIab-HQ-CPCB-HQ/Pvu2371, Environmental Laboratory RV Enviro International LLP,
Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285,
UPPCB-HQ/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. – 01, IMT, Kheri Sadh, Rohtak (Haryana) - 124001 India.		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT , GC, UV etc	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/WZ-17		Sample Collection Date: 16/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	QUALITY ASSURANCE QA MICRO ROOM
Sampling Code	--	--	WZ - 17
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	K	--	292
Acetone	mg/m ³	<1780	139
Ammonia	mg/m ³	<18	11
n-Butyl acetate	mg/m ³	<710	47
n-Butyl alcohol	mg/m ³	<150	08
Ethyl acetate	mg/m ³	<1400	42
Ethyl alcohol	mg/m ³	<1900	67
Formaldehyde	mg/m ³	<1.5	0.7
Isobutyl alcohol	mg/m ³	<150	54
Manganese dust and compounds (as Mn)	mg/m ³	<0.5	BDL
Phosphoric Acid	mg/m ³	<0.1	BDL
Pyridine	mg/m ³	<15	08
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	82
Phthalic Anhydride	mg/m ³	<0.1	BDL
Toluene	mg/m ³	<375	49
2 - Ethylhexanoic acid (2-EHA)	mg/m ³	<376	40
Butanol	mg/m ³	<152	51
Butyl Cellosolve	mg/m ³	<123	37
Ethyl Cellosolve Acetate	mg/m ³	<55	50
Mineral Turpentine Oil (MTO)	mg/m ³	<560	106
Acetic Acid	mg/m ³	<25	BDL
2 - Butanone (Methyl ethyl Ketone - MEK)	mg/m ³	<590	BDL
sec/tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	--	BDL
Nitric Acid	mg/m ³	<0.5	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	--	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<0.1	BDL

N. B. A. Methods Based on NIOSH, OSHA & CPCB.

B. Standard as per Fact Act 1948.

C. BDL :- <0.05 mg/m³

Sampling Done By Mr Shiv Singh & Mr Parshotam Singh.

Checked

R.P. Mahwah

EIL/Lab-In-Charge

Dr. Vipul Kumar



N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306

☎ : 9810098664, 9810725666, 9910233668

✉ : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC 17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India,
recognised as refn LB-2021/7/99/IIlab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP,
Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285,
UPPCB-HO/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. - 01, IMT, Kheri Sadh, Rohtak (Haryana) - 124001 India.		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT , GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EII/APL-R/01/26/WZ-15		Sample Collection Date: 16/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	QUALITY ASSURANCE QA GC ROOM
Sampling Code	--	--	WZ - 15
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	292
Acetone	mg/m ³	<1780	343
Ammonia	mg/m ³	<18	10
n-Butyl acetate	mg/m ³	<710	82
n-Butyl alcohol	mg/m ³	<150	52
Ethyl acetate	mg/m ³	<1400	94
Ethyl alcohol	mg/m ³	<1900	124
Formaldehyde	mg/m ³	<1.5	0.9
Isobutyl alcohol	mg/m ³	<150	68
Manganese dust and compounds (as Mn)	mg/m ³	<05	BDL
Phosphoric Acid	mg/m ³	<01	BDL
Pyridine	mg/m ³	<15	05
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	132
Phthalic Anhydride	mg/m ³	<01	BDL
Toluene	mg/m ³	<375	90
2 - Ethylhexanoic acid (2-EHA)	mg/m ³	<376	81
Butanol	mg/m ³	<152	57
Butyl Cellosolve	mg/m ³	<123	31
Ethyl Cellosolve Acetate	mg/m ³	<55	19
Mineral Turpentine Oil (MTO)	mg/m ³	<560	262
Acetic Acid	mg/m ³	<25	BDL
2 - Butanone (Methyl ethyl Ketone - MEK)	mg/m ³	<590	BDL
sec/tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	--	BDL
Nitric Acid	mg/m ³	<05	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	--	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<01	BDL

NN, B. A. Methods Based on NIOSH, OSHA & CPCB.
Sampling Done By Mr Shiv Singh & Mr Purohit Singh.

Checked

R.P. Narayan

B. Standard as per Fact Act 1948,

C. BDL :- <0.05 mg/m³



N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
 ☎ : 9810098664, 9810725666, 9910233668
 ✉ : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC-17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India,
recognised as refn LB-2021/7/99/IIab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP,
Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306 NABL TC-15285,
UPPCB-HO/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. – 01, IMT, Kheri Sadh, Rohtak (Harvata) – 124001 India.		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT, GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/WZ-28		Sample Collection Date: 16/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	Packing Area New Block
Sampling Code	--	--	WZ – 28
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	292
Acetone	mg/m ³	<1780	133
Ammonia	mg/m ³	<18	04
n-Butyl acetate	mg/m ³	<710	31
n-Butyl alcohol	mg/m ³	<150	08
Ethyl acetate	mg/m ³	<1400	83
Ethyl alcohol	mg/m ³	<1900	50
Formaldehyde	mg/m ³	<1.5	0.3
IsoButyl alcohol	mg/m ³	<150	04
Manganese dust and compounds (as Mn)	mg/m ³	<0.5	BDL
Phosphoric Acid	mg/m ³	<0.1	BDL
Pyridine	mg/m ³	<15	BDL
Methyl Isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	36
Phthalic Anhydride	mg/m ³	<0.1	BDL
Toluene	mg/m ³	<375	72
2 – Ethylhexanoic acid (2-EHA)	mg/m ³	<376	31
Butanol	mg/m ³	<152	49
Butyl Cellosolve	mg/m ³	<123	21
Ethyl Cellosolve Acetate	mg/m ³	<55	BDL
Mineral Turpentine Oil (MTO)	mg/m ³	<560	109
Acetic Acid	mg/m ³	<25	BDL
2 – Butanone (Methyl ethyl Ketone – MEK)	mg/m ³	<590	BDL
sec/tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	--	BDL
Nitric Acid	mg/m ³	<0.5	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	--	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<0.1	BDL


NN. B. A. Methods Based on NIOSH, OSHA & CPCB.
Sampling Done By Mr Shiv Singh & Mr Purshotam Singh.

B. Standard as per Fact Act 1948.

C. BDL :- <0.05 mg/m³

Checked

R.P. Marwah



N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
 : 9810098664, 9810725666, 9910233668
 : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC-17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India,
recognised as refn LB-2021/7/99/IIlab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP,
Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285,
UPPCB-HO/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. – 01, IMT, Kheri Sadh, Rohat (Haryana) – 124001 India.		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT , GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/WZ-27		Sample Collection Date: 16/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	Packing Area Old Block
Sampling Code	--	--	WZ- 27
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	292
Acetone	mg/m ³	<1780	139
Ammonia	mg/m ³	<18	07
n-Butyl acetate	mg/m ³	<710	93
n-Butyl alcohol	mg/m ³	<150	12
Ethyl acetate	mg/m ³	<1400	76
Ethyl alcohol	mg/m ³	<1900	88
Formaldehyde	mg/m ³	<1.5	0.9
Isobutyl alcohol	mg/m ³	<150	15
Manganese dust and compounds (as Mn)	mg/m ³	<05	BDL
Phosphoric Acid	mg/m ³	<01	BDL
Pyridine	mg/m ³	<15	07
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	82
Phthalic Anhydride	mg/m ³	<01	BDL
Toluene	mg/m ³	<375	29
2 – Ethylhexanoic acid (2-EHA)	mg/m ³	<376	73
Butanol	mg/m ³	<152	34
Butyl Cellosolve	mg/m ³	<123	48
Ethyl Cellosolve Acetate	mg/m ³	<55	13
Mineral Turpentine Oil (MTO)	mg/m ³	<560	147
Acetic Acid	mg/m ³	<25	BDL
2 – Butanone (Methyl ethyl Ketone – MEK)	mg/m ³	<590	BDL
sec/tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	--	BDL
Nitric Acid	mg/m ³	<05	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<200	BDL
Cyclohexanol	mg/m ³	--	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<01	BDL

N. B. A. Methods Based on NIOSH, OSHA & CPCB.

B. Standard as per Fact Act 1948.

C. BDL :- <0.05 mg/m³

Sampling Done By Mr Shiv Singh & Mr Purshotam Singh.

Checked

R.P. Marwah

EIL/Lab-In-Charge

Dr. Vipul Kumar



N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 305
 ☎ : 9810098664, 9810725666, 9910233668
 ✉ : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC-17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India,
recognised as refn LB-2021/7/99/IIab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP,
Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285,
UPPCB-HO/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. - 01, IMT, Kheri Sadh, Rohtak (Haryana) - 124001 India..		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT , GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/WZ-22		Sample Collection Date: 16/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	BG-2 OLD BLOCK
Sampling Code	--	--	WZ - 22
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	292
Acetone	mg/m ³	<1780	240
Ammonia	mg/m ³	<18	09
n-Butyl acetate	mg/m ³	<710	120
n-Butyl alcohol	mg/m ³	<150	109
Ethyl acetate	mg/m ³	<1400	187
Ethyl alcohol	mg/m ³	<1900	136
Formaldehyde	mg/m ³	<1.5	0.8
Isobutyl alcohol	mg/m ³	<150	90
Manganese dust and compounds (as Mn)	mg/m ³	<05	BDL
Phosphoric Acid	mg/m ³	<01	BDL
Pyridine	mg/m ³	<15	05
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	151
Phthalic Anhydride	mg/m ³	<01	BDL
Toluene	mg/m ³	<375	131
2 - Ethylhexanoic acid (2-EHA)	mg/m ³	<376	127
Butanol	mg/m ³	<152	60
Butyl Cellosolve	mg/m ³	<123	104
Ethyl Cellosolve Acetate	mg/m ³	<55	37
Mineral Turpentine Oil (MTO)	mg/m ³	<560	181
Acetic Acid	mg/m ³	<25	BDL
2 - Butanone (Methyl ethyl Ketone - MEK)	mg/m ³	<590	BDL
sec/tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	--	BDL
Nitric Acid	mg/m ³	<05	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	--	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<01	BDL

N.B. A. Methods Based on NIOSH, OSHA & CPCB. B. Standard as per Fact Act 1948. C. BDL > <0.05 mg/m³

Sampling Done By Mr Shiv Singh & Mr Purshotam Singh.

Checked

R.P. Marwah

EN/Lab-In-Charge

Dr. Vipul Kumar

N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
 ☎ : 9810098664, 9810725666, 9910233668
 ✉ : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISOREG-17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India,
recognised as refn LB-2021/7/99/IIab-HO-CPCB-HQ/Pvt/2371, Environmental Laboratory RV Enviro International LLP,
Plot No. 136, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285,
UPPCB-HO/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. - 01, IMT, Kheri Sadh, Rohtak (Haryana) - 124001 India.		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT , GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/WZ-21		Sample Collection Date: 16/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	BG-2 NEW BLOCK
Sampling Code	--	--	WZ - 21
Sampling Duration	--	--	180 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	292
Acetone	mg/m ³	<1780	250
Ammonia	mg/m ³	<18	08
n-Butyl acetate	mg/m ³	<710	162
n-Butyl alcohol	mg/m ³	<150	69
Ethyl acetate	mg/m ³	<1400	93
Ethyl alcohol	mg/m ³	<1900	141
Formaldehyde	mg/m ³	<1.5	0.7
Isobutyl alcohol	mg/m ³	<150	60
Manganese dust and compounds (as Mn)	mg/m ³	<0.5	BDL
Phosphoric Acid	mg/m ³	<0.1	BDL
Pyridine	mg/m ³	<15	07
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	183
Phthalic Anhydride	mg/m ³	<0.1	BDL
Toluene	mg/m ³	<375	145
2 - Ethylhexanoic acid (2-EHA)	mg/m ³	<376	121
Butanol	mg/m ³	<152	82
Butyl Cellosolve	mg/m ³	<123	71
Ethyl Cellosolve Acetate	mg/m ³	<55	27
Mineral Turpentine Oil (MTO)	mg/m ³	<560	219
Acetic Acid	mg/m ³	<25	BDL
2 - Butanone (Methyl ethyl Ketone - MEK)	mg/m ³	<590	BDL
sec/tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	--	BDL
Nitric Acid	mg/m ³	<0.5	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	--	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<0.1	BDL

N.B. A. Methods Based on NIOSH, OSHA & CPCB.

Sampling Done By Mr Shiv Singh & Mr Purshotam Singh.

Checked

R.P. Marwah

B. Standard as per Fact Act 1948.

C. BDL :- <0.05 mg/m³

EIL Lab-In-Charge

Dr. Anil Kumar

Noida

N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 136-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306

☎ : 9810098664, 9810725666, 9910233668

✉ : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC 17021 CB



— ENVIRO-INTERNATIONAL —

Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India, recognised as refn LB-2021/7/99/IIlab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP, Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285, UPPCB-HO/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018



TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. - 01, IMT, Kheri Sadh, Rohtak (Haryana) - 124001 India.		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT, GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/WZ-8		Sample Collection Date: 15/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	POLYMER GROUND FLOOR OLD BLOCK
Sampling Code	--	--	WZ - 08
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	290
Acetone	mg/m ³	<1780	187
Ammonia	mg/m ³	<18	05
n-Butyl acetate	mg/m ³	<710	92
n-Butyl alcohol	mg/m ³	<150	13
Ethyl acetate	mg/m ³	<1400	89
Ethyl alcohol	mg/m ³	<1900	137
Formaldehyde	mg/m ³	<1.5	0.7
Isobutyl alcohol	mg/m ³	<150	64
Manganese dust and compounds (as Mn)	mg/m ³	<0.5	BDL
Phosphoric Acid	mg/m ³	<0.1	BDL
Pyridine	mg/m ³	<15	12
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	80
Phthalic Anhydride	mg/m ³	<0.1	BDL
Toluene	mg/m ³	<375	126
2 - Ethylhexanoic acid (2-EHA)	mg/m ³	<376	31
Butanol	mg/m ³	<152	58
Butyl Cellosolve	mg/m ³	<123	46
Ethyl Cellosolve Acetate	mg/m ³	<55	21
Mineral Turpentine Oil (MTO)	mg/m ³	<560	198
Acetic Acid	mg/m ³	<25	BDL
2 - Butanone (Methyl ethyl Ketone - MEK)	mg/m ³	<590	BDL
sec/tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	--	BDL
Nitric Acid	mg/m ³	<0.5	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	--	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<0.1	BDL

N. B. A. Methods Based on NIOSH, OSHA & CPCB. B. Standard as per Fact Act 1948. C. BDL :- <0.05 mg/m³

Sampling Done By Mr Shiv Singh & Mr Purshotam Singh.

Checked

R.P. Marwah

EIL/Lab-In-Charge

Dr. Vipul Kumar

Greater Noida

N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
: 9810098664, 9810725666, 9910233668
: vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC-17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India,
recognised as refn LB-2021/7/99/IIlab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP,
Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285,
UPPCB-HO/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. - 01, IMT, Kheri Sadh, Rohtak (Haryana) - 124001 India..		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT , GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/WZ-9		Sample Collection Date: 15/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	POLYMER GROUND FLOOR NEW BLOCK
Sampling Code	--	--	WZ - 09
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	290
Acetone	mg/m ³	<1780	204
Ammonia	mg/m ³	<18	14
n-Butyl acetate	mg/m ³	<710	60
n-Butyl alcohol	mg/m ³	<150	11
Ethyl acetate	mg/m ³	<1400	96
Ethyl alcohol	mg/m ³	<1900	106
Formaldehyde	mg/m ³	<1.5	0.8
Isobutyl alcohol	mg/m ³	<150	09
Manganese dust and compounds (as Mn)	mg/m ³	<0.5	BDL
Phosphoric Acid	mg/m ³	<01	BDL
Pyridine	mg/m ³	<15	12
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	78
Phthalic Anhydride	mg/m ³	<01	BDL
Toluene	mg/m ³	<375	122
2 - Ethylhexanoic acid (2-EHA)	mg/m ³	<376	71
Butanol	mg/m ³	<152	12
Butyl Cellosolve	mg/m ³	<123	56
Ethyl Cellosolve Acetate	mg/m ³	<55	32
Mineral Turpentine Oil (MTO)	mg/m ³	<560	198
Acetic Acid	mg/m ³	<25	BDL
2 - Butanone (Methyl ethyl Ketone - MEK)	mg/m ³	<590	BDL
sec/tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	--	BDL
Nitric Acid	mg/m ³	<0.5	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	--	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<01	BDL

N. B. A. Methods Based on NIOSH, OSHA & CPCB.
Sampling Done By Mr Shiv Singh & Mr Purshotam Singh.
Checked

R.P. Marwaha

B. Standard as per Fact Act 1948.

C. BML :- <0.05 mg/m³

Signature of In-Charge
Dr. Vipul Kumar
Greater Noida

N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
Q : 9810098664, 9810725666, 9910233668
✉ : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC 17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India,
recognised as rin LB-2021/7/99/Ilab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP,
Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285,
UPPCB-HO/609/CC/89/2009-10/2023, ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. – 01, IMT, Kheri Sadh, Rohtak (Haryana) – 124001 India.		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT , GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/VZ-10		Sample Collection Date: 15/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	POLYMER 1st FLOOR OLD BLOCK
Sampling Code	--	--	WZ – 10
Sampling Duration	--	--	400 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	290
Acetone	mg/m ³	<1780	193
Ammonia	mg/m ³	<18	09
n-Butyl acetate	mg/m ³	<710	87
n-Butyl alcohol	mg/m ³	<150	09
Ethyl acetate	mg/m ³	<1400	94
Ethyl alcohol	mg/m ³	<1900	78
Formaldehyde	mg/m ³	<1.5	0.2
Isobutyl alcohol	mg/m ³	<150	23
Manganese dust and compounds (as Mn)	mg/m ³	<0.5	BDL
Phosphoric Acid	mg/m ³	<0.1	BDL
Pyridine	mg/m ³	<15	11
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	90
Phthalic Anhydride	mg/m ³	<0.1	BDL
Toluene	mg/m ³	<375	106
2 – Ethylhexanoic acid (2-EHA)	mg/m ³	<376	70
Butanol	mg/m ³	<152	47
Butyl Cellosolve	mg/m ³	<123	59
Ethyl Cellosolve Acetate	mg/m ³	<55	31
Mineral Turpentine Oil (MTO)	mg/m ³	<560	206
Acetic Acid	mg/m ³	<25	BDL
2 – Butanone (Methyl ethyl Ketone – MEK)	mg/m ³	<590	BDL
sec/tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	–	BDL
Nitric Acid	mg/m ³	<0.5	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	–	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<0.1	BDL

N. B. A. Methods Based on NIOSH, OSHA & CPCB. B. Standard as per Fact Act 1948. C. BDL :- <0.05 mg/m³

Sampling Done By Mr Shiv Singh & Mr Purshotam Singh.

Checked

R.P. Marwah

EIL Lab-In-Charge
 Dr. Vipul Kumar
 Greater Noida

N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
 ☎ : 9810098664, 9810725666, 9910233668
 ✉ : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC 17025 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India,
recognised as rin LB-2021/7/99/IIab-HO-CPCB-HO/PvU2371, Environmental Laboratory RV Enviro International LLP,
Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285,
UPPCB-HO/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. – 01, IMT, Kheri Sadh, Rohtak (Haryana) – 124001 India .		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT , GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/WZ-11		Sample Collection Date: 15/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	POLYMER 1st FLOOR NEW BLOCK
Sampling Code	--	--	WZ – 11
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	K	--	290
Acetone	mg/m ³	<1780	218
Ammonia	mg/m ³	<18	07
n-Butyl acetate	mg/m ³	<710	72
n-Butyl alcohol	mg/m ³	<150	57
Ethyl acetate	mg/m ³	<1400	19
Ethyl alcohol	mg/m ³	<1900	31
Formaldehyde	mg/m ³	<1.5	0.7
Isobutyl alcohol	mg/m ³	<150	22
Manganese dust and compounds (as Mn)	mg/m ³	<05	BDL
Phosphoric Acid	mg/m ³	<01	BDL
Pyridine	mg/m ³	<15	12
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	91
Phthalic Anhydride	mg/m ³	<01	BDL
Toluene	mg/m ³	<375	106
2 – Ethylhexanoic acid (2-EHA)	mg/m ³	<376	93
Butanol	mg/m ³	<152	73
Butyl Cellosolve	mg/m ³	<123	74
Ethyl Cellosolve Acetate	mg/m ³	<55	39
Mineral Turpentine Oil (MTO)	mg/m ³	<560	187
Acetic Acid	mg/m ³	<25	BDL
2 – Butanone (Methyl ethyl Ketone – MEK)	mg/m ³	<590	BDL
sec/tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	–	BDL
Nitric Acid	mg/m ³	<05	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	–	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<01	BDL

NN. B. A. Methods Based on NIOSH, OSHA & CPCB. B. Standard as per Fact Act 1948. C. BDL :- <0.05 mg/m³

Sampling Done By Mr Shlv Singh & Mr Purshotam Singh.

Checked

R.P. Marwah

EIL Lab-In-Charge

Dr. Vipul Kumar

ter

N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
: 9810098664, 9810725666, 9910233668
✉ : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC-17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India,
recognised as refn LB-2021/7/99/IIlab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP,
Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285,
UPPCB-HO/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. - 01, IMT, Kheri Sadh, Rohtak (Haryana) - 124001 India.,		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT , GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/WZ-12		Sample Collection Date: 15/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	POLYMER IInd FLOOR OLD BLOCK
Sampling Code	--	--	WZ - 12
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	290
Acetone	mg/m ³	<1780	236
Ammonia	mg/m ³	<18	13
n-Butyl acetate	mg/m ³	<710	99
n-Butyl alcohol	mg/m ³	<150	65
Ethyl acetate	mg/m ³	<1400	72
Ethyl alcohol	mg/m ³	<1900	90
Formaldehyde	mg/m ³	<1.5	0.6
Isobutyl alcohol	mg/m ³	<150	73
Manganese dust and compounds (as Mn)	mg/m ³	<85	BDL
Phosphoric Acid	mg/m ³	<81	BDL
Pyridine	mg/m ³	<15	12
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	43
Phthalic Anhydride	mg/m ³	<81	BDL
Toluene	mg/m ³	<375	127
2 - Ethylhexanoic acid (2-EHA)	mg/m ³	<376	46
Butanol	mg/m ³	<152	103
Butyl Cellosolve	mg/m ³	<123	61
Ethyl Cellosolve Acetate	mg/m ³	<55	15
Mineral Turpentine Oil (MTO)	mg/m ³	<560	227
Acetic Acid	mg/m ³	<25	BDL
2 - Butanone (Methyl ethyl Ketone - MEK)	mg/m ³	<590	BDL
sec./tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Flouride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	--	BDL
Nitric Acid	mg/m ³	<85	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	--	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<81	BDL

NN. B. A. Methods Based on NIOSH, OSHA & CPCB. B. Standard as per Fact Act 1948. C. BDL :- <0.05 mg/m³
 Sampling Done By Mr Shiv Singh & Mr Purshotam Singh.

Checked

R.P. Marwah



N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
 : 9810098664, 9810725666, 9910233668
 : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC 17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India,
recognised as refn LB-2021/7/99/IIab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP,
Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B Nagar-UP 201306, NABL TC-15285,
UPPCB-HO/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. - 01, IMT, Kheri Sadh, Rohtak (Haryana) - 124001 India.		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT, GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/API-R/01/26/WZ-19		Sample Collection Date: 15/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	BG-1 NEW BLOCK
Sampling Code	--	--	WZ - 19
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	290
Acetone	mg/m ³	<1780	329
Ammonia	mg/m ³	<18	14
n-Butyl acetate	mg/m ³	<710	161
n-Butyl alcohol	mg/m ³	<150	101
Ethyl acetate	mg/m ³	<1400	214
Ethyl alcohol	mg/m ³	<1900	235
Formaldehyde	mg/m ³	<1.5	1.1
Isobutyl alcohol	mg/m ³	<150	146
Manganese dust and compounds (as Mn)	mg/m ³	<85	BDL
Phosphoric Acid	mg/m ³	<01	BDL
Pyridine	mg/m ³	<15	09
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	230
Phthalic Anhydride	mg/m ³	<01	BDL
Toluene	mg/m ³	<375	128
2 - Ethylhexanoic acid (2-EHA)	mg/m ³	<376	103
Butanol	mg/m ³	<152	82
Butyl Cellosolve	mg/m ³	<123	58
Ethyl Cellosolve Acetate	mg/m ³	<55	49
Mineral Turpentine Oil (MTO)	mg/m ³	<560	217
Acetic Acid	mg/m ³	<25	BDL
2 - Butanone (Methyl ethyl Ketone - MEK)	mg/m ³	<590	BDL
sec/tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	--	BDL
Nitric Acid	mg/m ³	<05	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	--	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<01	BDL

N. B. A. Methods Based on NIOSH, OSHA & CPQB. B. Standard as per Fact Act 1948. C. BDL :- <0.05 mg/m³

Sampling Done By Mr Shiv Singh & Mr Purshotam Singh.

Checked

R.P. Marwah

EIL/Lab-In-Charge
Dr. Vipul Kumar
G. Noida

NOTE:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
☎ : 9810098664, 9810725666, 9910233668
✉ : vipul_kumar4@rediffmail.com | envirointernational@ec@gmail.com



ISO/IEC 17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India, recognised as refn LB-2021/7/99/IIlab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP, Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285, UPPCB-HO/600/GC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO :
M/s ASIAN PAINTS LIMITED
Plot No. - 01, IMT, Kheri Sadh,
Rohtak (Haryana) - 124001 India.

Sample Details : VOC-TWA
Sample Reference: EIL/APL-R/01/26/WZ-20

SUBJECT : VOC-TWA
METHODS : Based on NIOSH, OSHA
INSTRUMENTS: Handy Sampler, CT, GC, UV etc.

Sample Collection Date: 15/01/26
Sample Reporting Date: 30/01/26

ANALYSIS REPORT

SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	BG-1 OLD BLOCK
Sampling Code	--	--	WZ - 20
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	290
Acetone	mg/m ³	<1780	304
Ammonia	mg/m ³	<18	09
n-Butyl acetate	mg/m ³	<710	187
n-Butyl alcohol	mg/m ³	<150	109
Ethyl acetate	mg/m ³	<1400	132
Ethyl alcohol	mg/m ³	<1900	190
Formaldehyde	mg/m ³	<1.5	0.8
Isobutyl alcohol	mg/m ³	<150	70
Manganese dust and compounds (as Mn)	mg/m ³	<05	BDL
Phosphoric Acid	mg/m ³	<01	BDL
Pyridine	mg/m ³	<15	09
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	133
Phthalic Anhydride	mg/m ³	<01	BDL
Toluene	mg/m ³	<375	90
2 - Ethylhexanoic acid (2-EHA)	mg/m ³	<376	81
Butanol	mg/m ³	<152	78
Butyl Cellosolve	mg/m ³	<123	94
Ethyl Cellosolve Acetate	mg/m ³	<55	46
Mineral Turpentine Oil (MTO)	mg/m ³	<560	221
Acetic Acid	mg/m ³	<25	BDL
2 - Butanone (Methyl ethyl Ketone - MEK)	mg/m ³	<590	BDL
sec/tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	--	BDL
Nitric Acid	mg/m ³	<05	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	--	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<01	BDL

N. B. A. Methods Based on NIOSH, OSHA & CPCB. B. Standard as per Fact Act 1948. C. BDL :- <0.05 mg/m³

Sampling Done By Mr Shiv Singh & Mr Purshotam Singh.

Checked

R.P. Marwah

EIL/Lab-In-Charge

Dr. Vipul Kumar

ter
Nia

N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
☎ : 9810098664, 9810725666, 9910233668
✉ : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC-17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India,
recognised as r/n LB-2021/7/99/IIlab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP,
Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285,
UPPCB-HO/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. - 01, IMT, Kheri Sadh, Rohtak (Haryana) - 124001 India.	SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT, GC, UV etc.
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/WZ-4	Sample Collection Date: 14/01/26 Sample Reporting Date: 30/01/26

ANALYSIS REPORT

SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	WPB 1st FLOOR OLD BLOCK
Sampling Code	--	--	WZ - 04
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	289
Acetone	mg/m ³	<1780	164
Ammonia	mg/m ³	<18	06
n-Butyl acetate	mg/m ³	<710	80
n-Butyl alcohol	mg/m ³	<150	12
Ethyl acetate	mg/m ³	<1400	109
Ethyl alcohol	mg/m ³	<1900	76
Formaldehyde	mg/m ³	<1.5	0.7
IsoButyl alcohol	mg/m ³	<150	64
Manganese dust and compounds (as Mn)	mg/m ³	<05	BDL
Phosphoric Acid	mg/m ³	<01	BDL
Pyridine	mg/m ³	<15	06
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	164
Phthalic Anhydride	mg/m ³	<01	BDL
Toluene	mg/m ³	<375	71
2 - Ethylhexanoic acid (2-EHA)	mg/m ³	<376	44
Butanol	mg/m ³	<152	37
Butyl Cellosolve	mg/m ³	<123	96
Ethyl Cellosolve Acetate	mg/m ³	<55	31
Mineral Turpentine Oil (MTO)	mg/m ³	<560	161
Acetic Acid	mg/m ³	<25	BDL
2 - Butanone (Methyl ethyl Ketone - MEK)	mg/m ³	<590	BDL
sec/tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	--	BDL
Nitric Acid	mg/m ³	<05	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	--	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<01	BDL

N. B. A. Methods Based on NIOSH, OSHA & CPCB. B. Standard as per Fact Act 1948. C. BDL :- <0.05 mg/m³

Sampling Done By Mr Shiv Singh & Mr Purshotam Singh,
Checked

R.P. Marwah

EIL/Lab-In-Charge
Dr. Vipul Kumar
Greater Noida

N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
: 9810098664, 9810725666, 9910233668
: vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC 17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India,
recognised as refn LB-20217/99/IIab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP,
Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285,
UPPCB-HO/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. - 01, IMT, Kheri Sadh, Rohtak (Haryana) - 124001 India.		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT, GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/WZ-5		Sample Collection Date: 14/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	WPB 1st FLOOR NEW BLOCK
Sampling Code	--	--	WZ - 05
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	28.9
Acetone	mg/m ³	<1780	153
Ammonia	mg/m ³	<18	10
n-Butyl acetate	mg/m ³	<710	67
n-Butyl alcohol	mg/m ³	<150	26
Ethyl acetate	mg/m ³	<1400	62
Ethyl alcohol	mg/m ³	<1900	80
Formaldehyde	mg/m ³	<1.5	0.6
Isobutyl alcohol	mg/m ³	<150	16
Manganese dust and compounds (as Mn)	mg/m ³	<05	BDL
Phosphoric Acid	mg/m ³	<01	BDL
Pyridine	mg/m ³	<15	05
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	119
Phthalic Anhydride	mg/m ³	<01	BDL
Toluene	mg/m ³	<375	92
2 - Ethylhexanoic acid (2-EHA)	mg/m ³	<376	85
Butanol	mg/m ³	<152	57
Butyl Cellosolve	mg/m ³	<123	46
Ethyl Cellosolve Acetate	mg/m ³	<55	21
Mineral Turpentine Oil (MTO)	mg/m ³	<560	152
Acetic Acid	mg/m ³	<25	BDL
2 - Butanone (Methyl ethyl Ketone - MEK)	mg/m ³	<590	BDL
sec./tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	--	BDL
Nitric Acid	mg/m ³	<05	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	--	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<01	BDL

N. B. A. Methods Based on NIOSH, OSHA & CPCB. B. Standard as per Fact Act 1948. C. BDL :- <0.05 mg/m³
Sampling Done By Mr Shiv Singh & Mr Purshotam Singh.

Checked
R.P. Marwah

Lab-In-Charge
Dr. Vipul Kumar
Greater Noida

N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
9810098664, 9810725666, 9910233668
✉ vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC 17021 CB



ENVIRO-INTERNATIONAL



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India, recognised as refn LB-2021/7/99/llab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP, Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285, UPPCB-HO/600/CC/89/2009-10/2023, ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. – 01, IMT, Kheri Sadh, Rohtak (Haryana) – 124001 India.		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT , GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/WZ-6		Sample Collection Date: 14/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	WPB IInd FLOOR OLD BLOCK
Sampling Code	--	--	WZ – 06
Sampling Duration	--	--	400 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	289
Acetone	mg/m ³	<1780	124
Ammonia	mg/m ³	<18	06
n-Butyl acetate	mg/m ³	<710	68
n-Butyl alcohol	mg/m ³	<150	10
Ethyl acetate	mg/m ³	<1400	47
Ethyl alcohol	mg/m ³	<1900	32
Formaldehyde	mg/m ³	<1.5	0.7
Isobutyl alcohol	mg/m ³	<150	17
Manganese dust and compounds (as Mn)	mg/m ³	<05	BDL
Phosphoric Acid	mg/m ³	<01	BDL
Pyridine	mg/m ³	<15	09
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	31
Phthalic Anhydride	mg/m ³	<01	BDL
Toluene	mg/m ³	<375	41
2 – Ethylhexanoic acid (2-EHA)	mg/m ³	<376	27
Butanol	mg/m ³	<152	44
Butyl Cellosolve	mg/m ³	<123	31
Ethyl Cellosolve Acetate	mg/m ³	<55	18
Mineral Turpentine Oil (MTO)	mg/m ³	<560	96
Acetic Acid	mg/m ³	<25	BDL
2 – Butanone (Methyl ethyl Ketone – MEK)	mg/m ³	<590	BDL
sec/tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	--	BDL
Nitric Acid	mg/m ³	<05	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	--	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<01	BDL

N. B. A. Methods Based on NIOSH, OSHA & CPCB. B. Standard as per Fact Act 1948.

Sampling Done By Mr Shiv Singh & Mr Purshotam Singh.

C. BDL > <0.05 mg/m³

Checked

R.P. Marwah



N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
 : 9810098664, 9810725666, 9910233668
 : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC-17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India,
recognised as rin LB-2021/7/99/IIab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP,
Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B Nagar-UP 201306, NABL TC-15285,
UPPCB-HO/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. – 01, IMT, Kheri Sadh, Rohtak (Haryana) – 124001 India..		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT , GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/WZ-7		Sample Collection Date: 14/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	WPB II nd FLOOR NEW BLOCK
Sampling Code	--	--	WZ – 07
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	289
Acetone	mg/m ³	<1780	137
Ammonia	mg/m ³	<18	11
n-Butyl acetate	mg/m ³	<710	60
n-Butyl alcohol	mg/m ³	<150	05
Ethyl acetate	mg/m ³	<1400	92
Ethyl alcohol	mg/m ³	<1900	125
Formaldehyde	mg/m ³	<1.5	0.7
Isobutyl alcohol	mg/m ³	<150	57
Manganese dust and compounds (as Mn)	mg/m ³	< 05	BDL
Phosphoric Acid	mg/m ³	<01	BDL
Pyridine	mg/m ³	<15	03
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	< 0.184	BDL
Xylene	mg/m ³	<435	111
Phthalic Anhydride	mg/m ³	<01	BDL
Toluene	mg/m ³	<375	132
2 – Ethylhexanoic acid (2-EHA)	mg/m ³	<376	48
Butanol	mg/m ³	<152	30
Butyl Cellosolve	mg/m ³	<123	38
Ethyl Cellosolve Acetate	mg/m ³	<55	07
Mineral Turpentine Oil (MTO)	mg/m ³	<560	109
Acetic Acid	mg/m ³	<25	BDL
2 – Butanone (Methyl ethyl Ketone – MEK)	mg/m ³	<590	BDL
sec/tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Flouride as F	mg/m ³	< 2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	—	BDL
Nitric Acid	mg/m ³	<05	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	—	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<01	BDL

N. B. A. Methods Based on NIOSH, OSHA & CPCB. B. Standard as per Fact Act 1948. C. BDL <0.05 mg/m³

Sampling Done By Mr Shiv Singh & Mr Purshotam Singh.

Checked

R.P. Marwah

EIL Lab-In-Charge

Dr. Vipul Kumar

Greater
Noida

N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306

☎ : 9810098664, 9810725666, 9910233668

✉ : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO IEC-17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India, recognised as rin LB-2021/7/99/lab-HO-CPCB-HO/PvU/2371, Environmental Laboratory RV Enviro International LLP, Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285, UPPCB-HO/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. – 01, IMT, Kheri Sadh, Rohtak (Haryana) – 124001 India.		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT , GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R/01/26/WZ-26		Sample Collection Date: 14/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	WBP - PEL
Sampling Code	--	--	WZ - 26
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	280
Acetone	mg/m ³	<1780	167
Ammonia	mg/m ³	<18	12
n-Butyl acetate	mg/m ³	<710	99
n-Butyl alcohol	mg/m ³	<150	74
Ethyl acetate	mg/m ³	<1400	91
Ethyl alcohol	mg/m ³	<1900	132
Formaldehyde	mg/m ³	<1.5	0.6
Isobutyl alcohol	mg/m ³	<150	23
Manganese dust and compounds (as Mn)	mg/m ³	<0.5	BDL
Phosphoric Acid	mg/m ³	<0.1	BDL
Pyridine	mg/m ³	<1.5	0.7
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	82
Phthalic Anhydride	mg/m ³	<0.1	BDL
Toluene	mg/m ³	<375	57
2 - Ethylhexanoic acid (2-EHA)	mg/m ³	<376	64
Butanol	mg/m ³	<152	106
Butyl Cellosolve	mg/m ³	<123	64
Ethyl Cellosolve Acetate	mg/m ³	<55	33
Mineral Turpentine Oil (MTO)	mg/m ³	<560	181
Acetic Acid	mg/m ³	<25	BDL
2 - Butanone (Methyl ethyl Ketone - MEK)	mg/m ³	<590	BDL
sec./tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	--	BDL
Nitric Acid	mg/m ³	<0.5	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	--	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<0.1	BDL

N. B. A. Methods Based on NIOSH, OSHA & CPCB. B. Standard as per Fact Act 1948. C. BDL :- <0.05 mg/m³

Sampling Done By Mr Shiv Singh & Mr Parashotam Singh.

Checked

R.P. Marwah

EIL/Lab-In-Charge

Dr. Vipul Kumar

Signature

Date

Place

Signature

Date

Place

Signature

Date

Place

Signature

Date

Place

Signature

Date

Place

N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested sample.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306

☎ : 9810098664, 9810725666, 9910233668

✉ : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC-17021 CB



ENVIRO-INTERNATIONAL



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India, recognised as refn LB-2021/7/99/IIlab-HO-CPCB-HO/PvU/2371, Environmental Laboratory RV Enviro International LLP, Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285, UPPCB-HO/600/CC/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. – 01, IMT, Kheri Sadh, Rohatki (Uttar Pradesh) – 124001 India..		SUBJECT : VOC-TWA METHODS : Based on NIOSH, OSHA INSTRUMENTS: Handy Sampler, CT, GC, UV etc.	
Sample Details : VOC-TWA Sample Reference: EIL/APL-R /01/26/WZ-1		Sample Collection Date: 17/01/26 Sample Reporting Date: 30/01/26	
ANALYSIS REPORT			
SAMPLING SITE	UNIT	STANDARD/NORMS NIOSH	ETP CHEMICAL STORAGE ROOM
Sampling Code	--	--	WZ – 01
Sampling Duration	--	--	480 Minutes
Weather	--	--	Normal
Ambient Temperature	°K	--	293
Acetone	mg/m ³	<1780	139
Ammonia	mg/m ³	<18	06
n-Butyl acetate	mg/m ³	<710	53
n-Butyl alcohol	mg/m ³	<150	09
Ethyl acetate	mg/m ³	<1400	47
Ethyl alcohol	mg/m ³	<1900	90
Formaldehyde	mg/m ³	<1.5	0.6
Isobutyl alcohol	mg/m ³	<150	37
Manganese dust and compounds (as Mn)	mg/m ³	<0.5	BDL
Phosphoric Acid	mg/m ³	<0.1	BDL
Pyridine	mg/m ³	<15	BDL
Methyl isobutyl ketone (MIBK)	mg/m ³	<205	BDL
Ethylene Oxide	mg/m ³	<0.184	BDL
Xylene	mg/m ³	<435	42
Phthalic Anhydride	mg/m ³	<0.1	BDL
Toluene	mg/m ³	<375	64
2 – Ethylhexanoic acid (2-EHA)	mg/m ³	<376	58
Butanol	mg/m ³	<152	09
Butyl Cellosolve	mg/m ³	<123	17
Ethyl Cellosolve Acetate	mg/m ³	<55	09
Mineral Turpentine Oil (MTO)	mg/m ³	<560	128
Acetic Acid	mg/m ³	<25	BDL
2 – Butanone (Methyl ethyl Ketone – MEK)	mg/m ³	<590	BDL
sec/tert. Butyl Acetate	mg/m ³	<950	BDL
Chromic Acid & Chromates as Cr	mg/m ³	<0.05	BDL
Dibutyl Phthalate	mg/m ³	<5	BDL
Hydrogen Fluoride as F	mg/m ³	<2.5	BDL
Iron Oxide Fume (Fe ₂ O ₃)	mg/m ³	--	BDL
Nitric Acid	mg/m ³	<0.5	BDL
Phenol	mg/m ³	<19	BDL
Styrene	mg/m ³	<215	BDL
Methanol	mg/m ³	<260	BDL
Cyclohexanol	mg/m ³	--	BDL
Toluene diisocyanate (TDI)	mg/m ³	<0.142	BDL
Methyl Methacrylate	mg/m ³	<410	BDL
Lead	mg/m ³	<0.15	BDL
Chromium Metal & Insoluble Compound	mg/m ³	<0.1	BDL

N. B. A. Methods Based on NIOSH, OSHA & CPCB. B. Standard as per Fact Act 1948. C. BDL :- <0.05 mg/m³

Sampling Done By Mr Shiv Singh & Mr Purshotam Singh.

Checked

R.P. Mahwah

EIL/Lab-In-Charge
 Dr. Vipul Kumar
 Greater Noida

N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306

☎ : 9810098664, 9810725666, 9910233668

✉ : vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC 17021 CB

Annexure -3



Haryana State Pollution Control Board

SCF No. 42 & 43, Shopping Centre, Sector-6, Huda, Bahadurgarh Ph. 01276-243077 (O) Email:- hspcbrobdh@gmail.com



No. :HWM/ROH/2023/5743639

DT: 26/02/2023

To

M/s ASIAN PAINTS LIMITED

Asian Paints Limited, Plot No.1, Sector 30-B, HSIIDC, IMT Rohtak, 124021
Rohtak

Sub: Grant of Authorization under Hazardous and Other Wastes(Management & Transboundry Movement) Rules, 2016

1. Reference of application:5743639 dated: 26/02/2023
2. Amardeep Jain of ASIAN PAINTS LIMITED is hereby granted an authorization for generation, collection, storage, disposal on the premises situated at Asian Paints Limited, Plot No.1, Sector 30-B, HSIIDC, IMT Rohtak, 124021

Details of Authorization

S.No.	Name of process and Category of Hazardous Waste as per the Schedules I, II and III of these rules	Authorised mode of disposal or recycling or utilisation or co-processing, etc.	Quantity
1	cleaning, emptying and maintenance of petroleum oil storage tanks including, Oil-containing cargo residue, washing water and sludge	GEPIL	5 T/Annum
2	production and/or industrial use of solvents, Contaminated aromatic, aliphatic or napthenic solvents may or may not be fit for reuse	GEPIL	35 T/Annum
3	production and/or industrial use of solvents, Distillation residues	GEPIL	15 T/Annum
4	Industrial operations using mineral/synthetic oil as lubricant in hydraulic systems or other applications, Used/spent oil	RECYCLER	10 T/Annum
5	cleaning, emptying and maintenance of petroleum oil storage tanks including, Sludge and filters contaminated with oil	GEPIL	5 T/Annum
6	Production of asbestos or asbestos-containing materials, Discarded asbestos	GEPIL	2 T/Annum

7	Production and/or industrial use of paints, pigments, lacquers, varnishes and inks , Process wastes, residues & sludges	Pre processing / Co -processing	120 T/Annum
8	Production and/or industrial use of glues, cements, adhesive and resins, Wastes/residues (not made with vegetable or animal materials)	Pre processing / Co -processing	95 T/Annum
9	De-contamination of barrels/containers used for handling of hazardous waste/chemicals, Chemical Containing residue arising from decontamination	GEPIL	15 T/Annum
10	Handling of Hazardous chemicals and wastes, Empty barrels/containers/liners contaminated with hazardous chemicals/wastes	GEPIL & RECYCLER	77 T/Annum
11	Purification and treatment of exhaust air, water and waste water from the treatment plants (CETP's), Flue gas cleaning residue	GEPIL	2 T/Annum
12	Purification and treatment of exhaust air, water and waste water from the treatment plants (CETP's), Spent ion exchange resin containing toxic metal	GEPIL	5 T/Annum
13	Purification and treatment of exhaust air, water and waste water from the treatment plants (CETP's), Chemical sludge from waste water treatment	Pre processing / Co -processing	590 T/Annum
14	Purification and treatment of exhaust air, water and waste water from the treatment plants (CETP's), Oil and grease skimming residues	GEPIL & RECYCLER	15 T/Annum
15	Purification process for organic compounds/solvents, Spent carbon or filter medium	GEPIL	5 T/Annum

1. The authorization shall be valid for a period of 20/02/2023 to 30/09/2027
2. The authorization is subject to the following general and specific conditions :-

- (i) 1. Unit will submit agreement with GEPIL.
2. Unit will submit annual report under HWM Rules every year.
3. Unit will comply the conditions of HWM Rules.

**Regional Officer Bahadurgarh
For Haryana State Pollution Control Board**

Conditions of Authorization:

1. The authorised person shall comply with the provisions of the Environment (Protection) Act, 1986, and the rules made there under.
2. The authorization or its renewal shall be produced for inspection at the request of an officer authorised by the State Pollution Control Board.
3. The person authorised shall not rent, lend, sell, transfer or otherwise transport the hazardous and other wastes except what is permitted through this authorization.
4. Any unauthorised change in personnel equipment or working conditions as mentioned in the application by the person authorised shall constitute a breach of this authorization.
5. The person authorised shall implement Emergency Response Procedure (ERP) for which this authorization is being granted considering all site specific possible scenarios such as spillages, leakages, fire etc. and their possible impacts and also carry out mock drill in this regard at regular interval of time.
6. The person authorised shall comply with the provisions outlined in the Central Pollution Control Board guidelines on "Implementing Liabilities for Environmental Damages due to Handling and Disposal of Hazardous Waste and Penalty".
7. An application for the renewal of an authorization shall be made as laid down under these Rules.
8. Any other conditions for compliance as per the guidelines issued by the Ministry of Environment, Forest and Climate Changes or Central Pollution Control Board from time to time.
9. Annual return shall be filed by June 30 th for the period ensuring 31 st March of the year.

SHAKTI SINGH
Regional Officer Bahadurgarh
For Haryana State Pollution Control Board

Digitally signed by SHAKTI
SINGH
Date: 2023.02.26 19:07:00
+05'30'



Renewal
Certificate

A Luthra Group company
**GUJARAT ENVIRO PROTECTION
& INFRASTRUCTURE (HARYANA) Pvt.Ltd.**
CIN - U29197MH2005PTC262236
Near Pali-Mohabatbad Stone Crusher Zone,
Pali, Faridabad - 121004
Tel. : +91 129-4004954, +91 9711890001
e-mail : haryana@luthraindia.com



To whomsoever it may concern
This is to certify that

Certificate No : 4100003976

ASIAN PAINTS LTD

**PLOT NO - 01, SECTOR-30B,
IMT, VILLAGE - KHERISADH,
ROHTAK
Haryana**

is a valid member of

Gujarat Enviro-Protection And Infrastructure (Haryana) Pvt Limited

for Integrated Common Hazardous Waste Management Facility.

**This membership is valid for a period of
5 Years**

**For, Gujarat Enviro-Protection And Infrastructure (Haryana)
Pvt Limited**

Date of issue : 15.03.2021
Date of expiration : 14.03.2026
Place of Issue : SURAT

Director/Authorised signatory

Waste Information

SrNo	Type Of Waste	Sign Qty(TPA)	SrNo	Type Of Waste	Sign Qty(TPA)
1	CHEMICAL RESIDUE FROM DECONTAMINATION	10.000	2	CHEMICAL SLUDGE.	225.000
3	DISCARDED LINER CONTAINERS.	25.000	4	FILTER CONTAMINATED WITH OIL.	10.000
5	OIL & GREASE SKIMMING RESIDU.	5.000	6	OIL CONTAMINATED WITH WW SLUDGE	10.000
7	PROCESS WASTE.	125.000	8	SPENT CARBON.	5.000
9	WASTE RESIDUE.	80.000	10	WASTE SOLVENT.	30.000
				Total Sign Qty (TPA)	525.000

SUBJECT TO FARIDABAD JURISDICTION

Annexure -4

Date of purchase of stamp paper 10/12/2007
Total cost of plot - Rs. 80,15,67,000.00
Stamp duty @ 5% - Rs. 4,00,78,350.00

CONVEYANCE DEED

This deed of conveyance made and executed on the 31st day of December in the year 2008 between the Haryana State Industrial & Infrastructure Development Corporation Limited, Registered Office C-13 & 14, Sector-6, Panchkula, hereinafter called the transferor of the one part, which expression shall include its successor, assignees, administrators, executors through its authorized signatory; Mr.

Gulshan Kumar, Dy. General Manager (E) Bahadurgarh, Haryana State Industrial & Infrastructure Development Corporation Limited, having its registered office at 6A, Shantinagar, Santacruz East, Mumbai - 400055 (hereinafter called the transferee of the other part of the conveyance deed, which expression shall include his/her/its heirs, successors, assignees, administrators, nominees, executive etc. through its authorized signatory Mr. Jayesh Merchant S/o Mr. Tulsidas Merchant, resident of 4 Sai Manzil, 18 Almond Road, Mumbai - 400026.

Whereas the plot hereinafter described and intended to be hereby conveyed is owned by the transferor with full proprietary rights.

Whereas Industrial Plot No. 1, in I M T, - Rohtak (Industrial Model Township) measuring 129.285 Acres. was allotted to the transferee, in pursuance to its application for allotment of the plot for the purpose of setting up of Integrated paint manufacturing plant with final capacity of 400000 Kilo Liter per Annum as per the terms and conditions, contained in the Regular Letter of Allotment (RLA), dated 24th August 2008 and Agreement dated 6th November 2007 which shall continue to remain part and parcel of this deed

FOR ASIAN PAINTS LIMITED


JAYESH MERCHANT



Cy. Gen. Manager
HSIIDC
B. O. Bahadurgarh

Whereas the transferee has made the full payment amounting to Rs.80,15,67,000/- (Rs. Eighty Crores Fifteen Lacs and Sixty Seven Thousands only) as on date, towards the full price of the said plot to the transferor.

NOW THEREFORE, this deed witness that for the purpose of carrying into effect the Regular Letter of Allotment (RLA) and the Agreement and further in consideration of the said sum of Rs. 80,15,67,000/- (Rs. Eighty Crores Fifteen Lacs and Sixty Seven Thousands only) paid by the transferee, the transferor hereby grants and conveys to the transferee all that part and parcel of plot No. 1, in I M T - Rohtak, measuring 129.285 Acres on the following terms and conditions :-

1. That any additional price of the aforesaid plot, as a consequence of enhancement in compensation that may be awarded by the Court (s) in the matters/cases arising out of the acquisition proceedings or any incidental or connected matter thereto, shall be payable by the transferee, in lump-sum, within 30 days from the date of issuance of demand notice, alongwith interest @15% p. a. or in the installments as per the Policy of the Corporation approved from time to time. In case if the amount will be deposited in installments, interest @ 15% p.a. will be charged. In case of default, penal interest @ 2% higher than the above rate on the defaulted amount for the defaulted period will also be charged.
2. That the aforesaid plot has been allotted on the "as is where is basis" and that the transferor will not be responsible for leveling uneven site; and that the transferee shall be liable to pay additional sum/money for any structure/super structure, trees & plants, boundary/compound wall or any other fixture that may be standing/existing thereon at the time of allotment, for which compensation, as assessed, had been paid by the transferor.

FOR ASIAN PAINTS LIMITED


JAYESH MERCHANT
CHIEF FINANCIAL OFFICER &
COMPANY SECRETARY


Dy. Gen. Manager


HSIIDC

O. O. Bahadurgarh

3. That the transferee shall be required to implement the project, for which the aforesaid plot has been allotted, within a period of three years from the date of offer of possession; and that implementation of the project shall mean the commencement of commercial production, after coverage of construction in accordance with the norms specified in the Estate Management Procedure – 2005, as amended from time to time (hereinafter called EMP) and installation of the plant and machinery.
4. That notwithstanding the period of three years stipulated qua implementation of the project on the plot, the allottee shall comply with the following norms:-
 - a) The allottee shall be required to take possession of plot, submit building plan and start construction at site within Six months of allotment.
 - b) The allottee shall raise construction at least to the extent of plinth level within one Year of allotment.
 - c) The allottee shall complete the minimum required construction for completion of project and finalize tie-up for procurement of plant and machinery within two years.
 - d) The allottee shall implement the project after constructing at least 25% of the permissible covered area and raising investment in fixed capital assets (minimum of Rs.100 crores) in the project as per project report within three years of allotment and submit documents in this regard to the corporation.

Upon failure on the part of allottee to adhere to the schedule/time available for implementation of the project and investment of minimum Rs.100 crores

FOR ASIAN PAINTS LIMITED



JAYESH MERCHANT
CHIEF FINANCIAL OFFICER &
COMPANY SECRETARY


Dy. Gen. Manager (E)
HSIIDC
O. Bahadurgarh

in fixed capital assets in the project, HSIIDC shall be competent to resume the aforesaid plot.

5. Keeping in view that the aforesaid plot has been allotted under the ongoing scheme as per the provisions of EMP-2005; cost of the project being more than Rs.780 crores, the allottee hereby agrees and undertakes to implement the project within the stipulated period with an investment of Rs.500 crores as provided in the project report, failing which, the afore said plot shall be liable to the resumed. However, extension for implementation of project/raising investment in fixed capital assets as per project report can be considered under exceptional circumstances, subject to payment of extension fee at double the rates as stipulated in the EMP-2005, which may be revised from time to time.
6. That the transferee shall be deemed to have completed the project if he, within the period available for implementation of the project, achieves construction coverage as per the norms specified in EMP and starts commercial production of the project after installation of plant & machinery. The transferee shall, within one month of completion of project, inform the concerned field office of the transferor, in writing, that the project has been completed, along with documentary proofs in this regard.
7. That the transferee shall use and utilize the aforesaid plot for the purposes for which it has been allotted and shall not change the nature of the project or related activities in any manner whatsoever, except with the prior permission, which may be granted by the transferor only after considering the ground (s) and such other factors, as contemplated in the EMP, provided that the transferee has paid requisite fee along with written request in this behalf. Violation, if any, shall entail resumption of the plot.

FOR ASIAN PAINTS LIMITED


JAYESH MERCHANT
CHIEF FINANCIAL OFFICER &
CORPORATE SECRETARY


B. O. Bahadurgarh
HSIIDC

8. That the transferee shall construct the building on the aforesaid plot after getting the building plans approved from the competent authority and the said building plans shall be approved in conformity with the building bye-laws, as applicable from time to time. However, before start of construction, the transferee shall submit a copy of the approved building plans to the transferor.
9. That the transferee shall apply for an occupation certificate in the concerned field office of transferor. Further, the procedure to grant occupation certificate shall be governed by the rules and regulations of Department of Town and Country Planning, Haryana, as amended from time to time.
10. That the use of the land and the building erected on the above said plot shall be governed by the zoning plan of the Estate. The permissible covered area shall be governed as per rules and regulations of the Department of Town and Country Planning, Haryana, as amended from time to time. Zoning violations and the deviation from the approved building plans at any stage shall cause a notice to rectify the breach by the transferee. In the event of non-compliance by the transferee, the aforesaid plot shall be liable to be resumed and the transferee shall be required to remove the plant and machinery within a period of two months from the order of the resumption at the cost and peril of the transferee.
11. That the transferee shall not bifurcate the aforesaid plot except with the prior permission of the transferor. Bifurcation of the plot shall, however, be governed and regulated in the manner as provided in the EMP. Bifurcation of shed shall not be allowed.

FOR ASIAN PAINTS LIMITED


JAYESH MERCHANT
CHIEF FINANCIAL OFFICER &
COMPANY SECRETARY


Dy. Gen. Manager (E)

HSIIDC

R.O. Bahadurgarh

12. That the transferee shall have no right to transfer the land and building standing thereon by way of sale of gift, mortgage, lease or any other way without specific written approval from the transferor.
13. That further alienation of the above said plot may be allowed by the transferor only after the expiry of one year from the date of commencement of commercial production, after coverage of construction in accordance with the norms specified in EMP and installation of the plant and machinery, subject to further condition that the person, who steps into the shoes of the transferee, shall not be allowed to further transfer the plot for atleast one year from the date of transfer of the aforesaid plot in his/her/its name. Such transfer shall, however, be subject to the compliance of provisions and payment of transfer fee as prescribed in the EMP, as revised from time to time.

No transfer fee would be leviable after the project of the transferee has been in commercial production for more than five years and is free from all encumbrances. However, prior permission of transferor shall be necessary for such transfer of the plot. The fee at the rates, prescribed from time to time in the EMP, shall however, be payable by the transferee.

14. That the transfer of the aforesaid plot, due to inheritance, succession upon the death of the transferee/majority share holders or the project has been taken over by a financial Institution may be allowed without charging transfer fee, but on the payment of processing fee at the rates as prescribed in the EMP, from time to time. The change of management by transfer of majority shareholding shall also be treated as transfer.

FOR ASIAN PAINTS LIMITED

JAYESH MERCHANT
CHIEF FINANCIAL OFFICER &
COMPANY SECRETARY

Dy. Gen. Manager (E)

HSIIDC

O. Baladurgarh

15. That for seeking permission for further transfer of the aforesaid plot, the transferee shall apply to the transferor along with following documents :-

- a) Original letter of allotment.
- b) Proposed agreement to sell.
- c) Project report of the proposed transferee, in case of any change of project.
- d) Statement of means of financing of the proposed transferee.

The transferee shall, however, be required to submit his request for the proposed transfer within a period of 30 days from the date of proposed Agreement to Sell, failing which a penalty equivalent to the transfer fee shall be imposed upon the transferee, while allowing such transfer. In case the transfer is allowed, the person who steps into the shoes of the transferee, shall be required to enter into a fresh Agreement with the transferor in respect of the industrial plot.

16. That the change in shareholding may be allowed only if the original allottee/transferee or his family members (spouse, son, daughter, wife, parents, brother, sister) retain a minimum of 51% share in the project/company/firm. In case the original allottee / transferee and his family fail to retain the prescribed share holding of 51%, it shall be deemed to be transfer, for which the transfer fee at the rates prescribed in EMP, from time to time shall be payable by the transferor.
17. That the transferee, being a private limited company, if becomes a public limited company and is listed with recognized stock exchange, the change in constitution may be allowed subject to the condition that the transferee or his associates (family members), retain the largest share holding and having management control, otherwise it shall be treated as a case of transfer and the

FOR ASIAN PAINTS LIMITED

JAYESH MERCHANT
CHIEF FINANCIAL OFFICER


Dy. Gen. Manager (E)
HSIIDC
O. Bahadurgarh

transfer fee at the rates prescribed in EMP, from time to time, shall be payable by the transferee.


18. That in order to ensure optimum utilization of the industrial areas/industrial estates, leasing/renting of the premises of the building may be allowed if the transferee has made construction as per the standard norms and has remained in production for one year. Such permission may be granted by the transferor on payment of leasing fee, as prescribed in the EMP, from time to time. However, prior approval of the transferor for leasing shall be mandatory.


19. That the number of leases on the aforesaid plot shall be permitted as per the provisions contained in EMP. The permission for leasing shall be valid for the period specified in the permission letter and after having obtained permission for leasing, the transferee shall be at liberty to change the tenants within the period so specified subject to the transferee keeping transferor informed about any change made in the tenancy and getting the project of the lessee/ tenant approved from transferor and payment of leasing fee as prescribed in the EMP, from time to time.

20. That the transferee shall have to take water for the unit set up and other area of the said plot from the water supply system of the transferor on payment in accordance with the rates fixed from time to time. The transferee shall not dig or install any tube well/bore-well within his plot/shed for meeting his water requirements.

21. That the transferor shall continue to be the owner of all mines and minerals, whatsoever including sub-soil water in or underneath the surface of the plot with all such rights and powers as may be necessary or expedient for the purpose of searching, working, obtaining, removing and enjoying the same at

FOR ASIAN PAINTS LIMITED


JAYESH MERCHANT
DIRECTOR


Dy. Gen. Manager (E)

HSIDC

B. O. Bahadurgarh

all such times and in such manner as transferor may deem fit, with power to carry out any survey of all or any part of the said plot and to sink pits, erect building, construct lines and generally appropriate and use surface of the said plot for the purpose of doing the full enjoyment of the exceptions and reservations herein contained.

Provided that the transferee shall be entitled to receive from transferor such payment for the occupation by transferor of the surface and for the damage done to the surface or building on the said land by such works or workings or letting down as may be agreed upon between the transferor and the transferee or failing such agreement, the same shall be ascertained by reference to arbitration.

22. That the Government may in the near future acquire possession and proprietary rights over the land surrounding the industrial estates and the Government or any other authority on behalf of the Govt. may thereafter, in its discretion, decide to convert this area or a part thereof into a green belt or to use it for any other common purpose and in the event of such happening, the cost of the acquisition and development of the part of land so utilized payable by transferor to the Government or any authority on its behalf will be recoverable by transferor from its transferees proportionately. An amount demanded by transferor on account of such external development charges will be payable by the transferee to transferor in lump-sum or in installments, as may be decided by transferor.

23. That the transferee shall pay to the transferor such proportionate external development charges spent by the transferor or as may be payable to the Government or any other agency by the transferor for external water supply, electricity installation, Roads, Storm Water, drainage, sewerage, CETP, STP,

FOR ASIAN PAINTS LIMITED


JAYESH MERCHANT


Dy. Gen. Manager
HSIIDC
B. O. Bahadurgarh

pumping charges etc. , in addition to already stated in Clause 22 above, within 30 days from the date of the letter of demand failing which the transferee shall be liable to pay the sum along with interest @ 14% p.a. In the event of failure of the transferee to make payment of the amount demanded within three months from the date of issue of the said letter of demand, the plot shall be liable to be resumed.

24. That the transferor may, but its officers and servants, at all reasonable times and in reasonable manner after giving 24 hours notice in writing, enter in and upon any part of the plot and building erected thereon for the purpose of ascertaining that the transferee has duly performed and observed the conditions to be observed under the provisions of the RLA/Agreement and this deed.
25. That the transferor shall have full right, power and authority at all times, to do through its officers or servants, all acts and things which may be necessary or expedient for the purpose of enforcing compliance of all or any of the terms, conditions and reservations imposed and to recover from transferee, as first charge upon the said land, the cost of doing all or any such acts and things and all costs incurred in connection therewith or in any way relating thereto.
26. That the transferee shall comply with all the Estate Management regulations dealing with malba, cleanliness, quantum and the quality of effluent discharge, solid waste disposal, green cover obligations, vehicle parking regulations etc. among other things for proper maintenance of the industrial estate and its surrounding. Transferor shall be within its rights to ensure compliance of measures considered necessary for its maintenance and levy

FOR ASIAN PAINTS LIMITED


JAYESH MERCHANT
CHIEF FINANCIAL OFFICER &
COMPANY SECRETARY


Dy. Gen. Manager

HSIIC

R. O. Bahadurgarh

charges, fines and penalties, if necessary, towards achievement of its objectives.

27. That the transferee shall have to pay local and general taxes, rates or cesses etc., as imposed on the said plot by the competent authority from time to time.
28. That the transferee shall pay the proportionate maintenance and service charges fixed from time to time and as communicated by the transferor. The maintenance and service charges will be payable on per square meter basis.
29. That the transferee agrees and undertakes that he/she/it shall, as far as possible, employ 75% of un-skilled workforce and shall give preference for other categories to candidates from among the Haryana domiciles in the unit set up/to be set up on plot.
30. That the transferor transfers this plot for setting up and running an industry and thereby contributing to the overall economic activity in the State. In case the transferee does not continue to remain in production and the production gets held up, transferor shall issue a notice to resume production within a period of three months. In case the transferee fails to resume production activity within the given time, the plot shall be liable to be resumed.
31. That if the transferee appoints ANY ATTORNEY, he/she/they shall submit the certified copy of the Registered Power of Attorney along with photograph and signatures of the transferee duly attested by the Magistrate First Class within a week from the registration of the deed by Registered A/D post or in person.


FOR ASIAN PAINTS LIMITED


JAYESH MERCHANT
CHIEF FINANCIAL OFFICER &
COMPANY SECRETARY


Dy. Gen. Manager (E)
HSI/DC
S. O. Bahadurgarh

32. That so long as the transferee fully performs and complies with and continues to so perform and comply with each and all the terms and conditions herein made and provided, but not otherwise, the transferor will ensure to the transferee full and peaceful enjoyment of the rights and privileges herein and hereby conveyed in this deed.
33. That the transferor will be competent to resume plots in its Industrial Estates in case an transferee defaults in complying with the terms and conditions of allotment/transfer/leasing etc. The resumption of plot would be done by the transferor after giving show cause notice. Upon resumption, the principal amount deposited by the transferee will be refunded and deducting 10% of the price of the plot without any interest. The amount of interest and penalty, if any, paid on the installment (s), if any, shall also stand forfeited. The transferee will be free to remove the structure/debris, if any, within a period of two months of resumption order at his own cost, failing which it shall be removed by the transferor at the transferee's cost. The transferee shall not be entitled to any payment/compensation for building constructed by it on the resumed plot.
34. That the plot once resumed shall not be restored by transferor. However, an appeal shall lie to a committee, comprising of the Financial Commissioner Industries, Haryana, Director of Industries, Haryana and Managing Director, Haryana Financial Corporation against the order of the Transferor ordering resumption. The decision of the aforesaid committee shall be final and binding.
35. That all the acts and expenses of or incidental to the execution of this deed including the cost of stamp duty, registration etc. shall be borne by the transferee.



FOR ASIAN PAINTS LIMITED


JAYESH MERCHANT

Cy. Gen. Manager (E)

HSIDC
O. Bahadurgarh

Reg. No. 1574 Reg. Year 2008-2009 Book No. 1



विप्रेता
नितेन्द्र सिंह

क्रेता

गवाह

क्रेता
एशियन पेन्स लिमिटेड द्वारा कयेरा मर्वेट

गवाह 1:- दिवान सिंह नम्बरदार

गवाह 2:- श्याम कुमार

दिवान सिंह नम्बरदार

प्रमाण-पत्र

हनुमन्त सब रजिस्ट्रार
सांपला

प्रमाणित किया जाता है कि यह प्रलेख क्रमांक 1,574 आज दिनांक 31/12/2008 को बही न: 1 जिल्द न: 2 के पृष्ठ न: 195 पर पंजीकृत किया गया तथा इसकी एक प्रति अतिरिक्त बही सख्या 1 जिल्द न: 41 के पृष्ठ सख्या 83 से 95 पर चिपकाई गयी। यह भी प्रमाणित किया जाता है कि इस दस्तावेज के प्रस्तुतकर्ता और गवाहों ने अपने हस्ताक्षर/निशान अंगुल मेरे सामने किये हैं।

दिनांक 31/12/2008

हनुमन्त सब रजिस्ट्रार
उप/सयुक्त पंजीयन अधिकारी
सांपला

PROPOSED 30m. WIDE ROAD

PROPOSED 30m. WIDE ROAD

ASIAN PAINTS BRY. LIMIT

PLOT AREA : 129.285 Acres



FOR ASIAN PAINTS LIMITED

JAYESH MERCHANT
CHIEF FINANCIAL OFFICER &
COMPANY SECRETARY

Dy. Genl. Manager
BSI IDC
B. O. Behadurgarh

Annexure -5



— ENVIRO-INTERNATIONAL —

Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change, Govt of India, recognised as refn LB-2021/7/99/IIlab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP, Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285, UPPCB-HO/G00/CC/89/2009-10/2023, ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018



TEST REPORT


ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. - 01, IMT, Kheri Sadh, Rohtak (Haryana) - 124001 India.		SUBJECT : AMBIENT ZONE NOISE MONITORING PRINCIPLE & METHODS: Based on EPA: dB eq. INSTRUMENTS : Noise Level
Sample Details : Noise-Day Sample Reference: EIL/APL-R/01/26/WN - 71-80		Sample Collection Date: 21/01/26 Sample Reporting Date: 30/01/26
Sampling Station	Monitoring Report Day	Prescribed Standard As per EPA-1986 dB(A)
Near Gate No.1	62.7	75
Near Gate No 2	63.9	75
Near Gate No 3	60.5	75
Engg. Store	56.4	75
Putty Park	62.1	75
FPH Back Side	57.2	75
PMG Back Side	63.7	75
ETP Watch Tower	60.4	75
Storm Water Tank	62.4	75
Green Belt Area 1	57.3	75

Checked By

R.P. Marwah

EIL/Lab-In-Charge


Vipul Kumar



N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
9810098664, 9810725666, 9910233668
vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC 17021 CB



— ENVIRO-INTERNATIONAL —



Environment (Conservation) Act 1986 / CPCB-Ministry of Environment Forest & Climate Change Govt of India
recognised as refn LB-2021/7/99/IIab-HO-CPCB-HO/Pvt/2371, Environmental Laboratory RV Enviro International LLP,
Plot No. 138, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida, G.B. Nagar-UP 201306, NABL TC-15285,
UPPCB-HO/600/CG/89/2009-10/2023, ISO : 9001 : 2015, ISO : 14001 : 2015, ISO : 45001 : 2018

TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. - 01, IMT, Kheri Sadh, Rohtak (Haryana) - 124001 India.		SUBJECT : AMBIENT ZONE NOISE MONITORING PRINCIPLE & METHODS: Based on EPA: dB eq. INSTRUMENTS : Noise Level
Sample Details : Noise-Night Sample Reference: EIL/APL-R/01/26/WN - 81-90		Sample Collection Date: 21/01/26 Sample Reporting Date: 30/01/26
Sampling Station	Monitoring Report Night	Prescribed Standard As per EPA-1986 dB(A)
Near Gate No.1	58.0	70
Near Gate No 2	56.7	70
Near Gate No 3	58.1	70
Engg. Store	53.5	70
Putty Park	56.8	70
FPH Back Side	49.3	70
PMG Back Side	50.4	70
ETP Watch Tower	56.1	70
Storm Water Tank	50.0	70
Green Belt Area 1	55.8	70

Checked By
R.P. Marwah



N.B.:-

- The Sample/Samples received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
9810098664, 9810725666, 9910233668
vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC-17021 CB



— ENVIRO-INTERNATIONAL —



TEST REPORT

ISSUED TO : M/s ASIAN PAINTS LIMITED Plot No. - 01, IMT, Kheri Sadh, Rohtak (Haryana) - 124001 India..		SUBJECT : WORK ZONE NOISE MONITORING PRINCIPLE & METHODS: Based on EPA: dR eq INSTRUMENTS : Noise Level Meter	
Sample Details : Noise Sample Reference: EIL/APL-R/01/26/WN - 140		Sample Collection Date: 13/01/26 To 17/01/26 Sample Reporting Date: 24/01/26	
Sampling Station	Monitoring Report	Prescribed Standard As per Factories Act 1948 (For 8 hrs working in dB)	
Polymer Reactor R - 404 First Floor Old Block	77.5	90	
Polymer Pet R -404 First Floor Old Block	73.6	90	
Polymer Near URACA Pump First Floor New Block	80.1	90	
Polymer Pet R -414 First Floor New Block	73.7	90	
ETP Near Blower No.1	73.8	90	
PMG Crane 2 Front Side	72.4	90	
PMG Line no. 112	71.8	90	
Putty Plant Silo Area	76.3	90	
Utility Chiller Area R-502	86.9	90	
Utility Compressor R-503	85.3	90	
DG/GG R-502 & R 501	84.2	90	
Utility Boiler Area R 502	86.0	90	
Putty Plant BSM Powder Charging Area	78.2	90	
WBP Block Centre of TSD-107 & 108	73.2	90	
WBP Block Centre of TSD 105 & 106	80.5	90	
DG Area	77.3	90	
WBP Block TSD 114	70.0	90	
WBP Block Centre of 113-114	73.2	90	
Packing Area Line 104 Carton Maker.	78.2	90	
LQC Near Vibro Shaker	69.2	90	
PEL Lab TSD 50 Ltr.	74.4	90	
EHS Lab Near BOD Incubator	67.0	90	

N.B.

- The Sample Report received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off. & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
9810098664, 9810725666, 9910233668
vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO/IEC 17021 CR



— ENVIRO-INTERNATIONAL —



TEST REPORT

RM Lab GC Room Fume Hood	78.2	90
Instrument Room (Sonicator) QA Lab	84.5	90
PMQA drop test machine M/c	86.3	90
Packing Area near centre of line no. 105 & 108 Robot Area	75.7	90
Packing Area Line no 111 & 112 Filler Area	75.4	90
Packing g Area Line no 106	72.7	90
FPH (Fire Pump Hydrant Jockey Pump)	89.3	90
FPH (Fire Pump Man Electrical pump-1)	88.0	90
FPH (Fire Pump DG pump no 2)	86.4	90
PMG Denester DEN R 603 10 L/20L	79.3	90
RMG BLR 1210	83.4	90
Putty Plant Packing Line	87.5	90
RMG BLR 168	80.4	90
RMG FIBC - C	75.2	90
Finished Goods Area - Bridge Profiler PFST-2	76.3	90
Finished Goods Area - DAIFUKU Station	70.2	90
SILO Area Blower BLR -1231	85.4	90
SILO Area Blower- BLR-1215	89.7	90

Checked By
R.P. Marwah



N B:-

- The Sample/Results received shall be destroyed after 2 weeks unless specified otherwise.
- The Result indicated only refer to the tested samples.
- The Certificate shall not be used in any media or as evidence in the court of law.

Off & Lab : 138-139, Udyog Kendra-II Extn, Eco Tech-III, Greater Noida-201 306
9810098664, 9810725666, 9910233668
vipul_kumar4@rediffmail.com | envirointernationalec@gmail.com



ISO IEC 17021 CB

Annexure -6

Details of stock of Toxic/Hazardous Raw material with Quantity

S. No.	Raw Material Name	State	Means of Storage	Hazardous/toxic material		Safety Measures
				Quantity of storage(KL)	Days of storage(Avg)	
1	Pigment	Liquid/ Powder	Day tank Day bin	NA	NA	MSDS
2	Rutile	Powder	Silo	NA	NA	MSDS
3	Extender	Powder	Silo	NA	NA	MSDS
4	Additives	Liquid/ Powder	Silo , Tank, day tank , day bin	828.5	~77	MSDS
5	Monomer	Liquid	Tank , day tank	3300	~63	MSDS
6	Diesel	Liquid	Tank , day tank	200	Based on consumption	MSDS

Annexure -7



From: Compliance Rohtak <Compliance.Rohtak@aslanpaints.com>
Sent: Tuesday, September 30, 2025 6:00 PM
To: ronchd-mef@nc.in
Cc: ANAND OSWAL <anand.oswal@aslanpaints.com>; Kirti Tak <kirti.tak@aslanpaints.com>
Subject: Form V Submission- Aslan Paints Ltd. Rohtak

Dear Sir/Ms'am,

Please find attached the Environmental Statement- Form V for financial year ending 31st March 2025 as part of standard condition of EC(identification number- EC25B2601HR5779477N) dated 18th September 2025.

Regards
Kirti Tak
Manager-EHS
Aslan Paints Limited, Rohtak

Annexure -8

11th December, 2024

To
Regional Officer
Haryana State Pollution Control Board
SCO -A6,7 8, Near Vishal Hotel, Suncity, Sector-36
Rohtak, Haryana

Sub.: Submission of Eco-development Plan against our Environmental Clearance letter no. J-11011/1158/2007-IA (II), dated 09th April 2008 (referred hereafter as 'EC') for Integrated Paint Manufacturing plant at Plot No. 01, HSIIDC, IMT Rohtak, Haryana by M/s. Asian Paint Limited (referred hereafter as 'Unit')

Ref/Annexure:

- EC for Unit received as letter no. J-11011/1158/2007-IA (II), dated 09th April 2008
- Director – MoEFCC, Chandigarh, visit to the project site on dtd 25th July, 2024 and Certified Compliance report received on 07th October, 2024 against referred EC
- Eco-development report and Plan of Asian Paints Rohtak unit.

Dear Sir,

With reference to the subject matter, we are submitting a fresh Eco-development Plan against the general condition (Sr. NO. 12) mentioned in our Environmental Clearance for Approval.

As per the General condition (**Sr. No. 12**) mentioned in the Environment Clearance it states that:
"The company shall undertake eco-developmental measures including community welfare measures in the project area for the overall improvement of the environment. The eco-development plan should be submitted to the SPCB within 3 month of receipt of this letter for approval".

As we are unable to trace back the Eco-development plan documents in our archives, We are hereby submitting a fresh Eco-development plan that has been undertaken and planned by the Unit for your kind reference, record, and approval.

The non-availability of eco-development plan record has been identified as a non-compliance in the general condition (Sr. No. 12) mentioned in EC, Concluded compliance check conducted by the Director, MoEFCC, Chandigarh during his visit to the plant dtd 25th July 2024.

We would like to bring to your kind notice that we have been undertaking adequate eco-development measures right from the time of the plant commissioning i.e. from FY 2010-11 onwards till-date and plan to continue this as part of our commitment to the community.

Hereby kindly requesting to approve the eco-development plan.

Thanking you,

Yours faithfully,
For Asian Paints Limited
Authorized Signatory



RECEIVED
Asst./Clerk
20/12/24
Haryana State Pollution Control Board
ROHTAK

Eco-development plan & Report at Asian Paints Limited, Rohtak

Asian paints, being a responsible corporate citizen, is committed towards creating self-sustained, empowered, and equitable communities and has kept pace with the overall vision and mission delivering 'Joy' to people's life through its CSR interventions.

As an organization, we have formed partnerships with local NGOs and relevant stakeholders in assessing the requirements of local communities, to design program & its implementation, monitoring & evaluation. The **thematic focus areas** of Asian Paints Limited CSR programme are as follows:

- a) **Health & Hygiene:** Community health and hygiene is one of the key focus areas of our CSR activities. We aspire to deliver primary health care support through diagnosis and treatments to our communities. Our interventions are aimed at promoting preventive healthcare, building awareness about hygiene, sanitation, maternal and child health care. These interventions are carried out in the vicinity of manufacturing units of APL.
- b) **Water Security:** We acknowledge the significant problem of water scarcity in India, affecting millions of people. As a socially responsible company, we have placed a high priority on leaving a *Watermark* through holistic approach around water. We have been making efforts to address the challenges of water by not only reducing our consumption but also replenishing more than what we consume in our production processes. These interventions are carried out in the vicinity of manufacturing units of APL.
- c) **Skilling:** Asian Paints *Colour Academy* empowers communities with specialised skills by providing vocational training in the paint application trade. We have expanded our horizons in this segment to also include carpentry, plumbing and masonry trainings for the further benefit of our local communities to ensure enhanced livelihood. This is a Pan India intervention by Asian Paints with presence in 24 states with a total of 47 Mobile colour academies and 24 fixed colour academies.

During the year 2021-2024, APL has spent a total of **Rs.12.12 Cr** across various themes, all around the Haryana as a part of CSR activity. Asian Paints Limited is a listed company and a responsible corporate citizen and it will keep fulfilling its CSR requirements in the coming years as well.

The Set of Activities carried under various themes are as follows:

1. CSR interventions by APL in the vicinity of its manufacturing plant in Rohtak:

At the Asian Paints Rohtak Plant, CSR interventions have been carried out since 2010 around multiple thematic areas. In the previous financial year, Rohtak Plant has spent a total of Rs. 4.23 Crores across Water Security and Health & Hygiene thematic areas. Additionally, a total of Rs. 0.77 Cr was spent in Colour Academy in the state of Haryana.

The major projects carried out in the nearby locations of Rohtak Plant are:

Health & Hygiene:

- a) **Mobile Medical Unit:** This intervention is focused on providing primary/basic health care facilities to nearby villages ensuring quality health care services accessible to the marginalized community including disadvantaged older patients at no cost. In FY 2023-24, more than 20,000 beneficiaries were benefitted from this project by APL Rohtak.
- b) **Truckers Well-being Programme:** Through our *SAFAR* project, we focus on the wellbeing of trucker community by providing Consultation, Treatment, Medicines, Diagnosis, Referral; Physiotherapy, Nutrition and lifestyle counselling, Yoga and Nutrition sessions, Hygiene kit distribution; Awareness and facilitation for Scheme linkages etc. This intervention by APL Rohtak has helped more than 8500 Truckers in FY 2023-24.

- c) Nutrition Centric Interventions: Through this intervention, we focus to improve the health status, reduction in anaemia & malnutrition among adolescent girls, pregnant & lactating women (Women Reproductive Age Group: 15-49 Years) & Children with the support of AAAs (Anganwadi Workers, Accredited Social Health Activist & Auxiliary Nurse Midwife) in the nearby villages of APL Rohtak through counselling on food groups & diet diversity and Behaviour Change Communication (BCC). The target beneficiaries of this intervention in 2023-24 were more than 2000 women, children and adolescent girls.
- d) The total CSR spend after Health and hygiene during 2021-2024 are as follows:

Year	Thrust Area	Name of the project	Amount Released FY 2021-24
2021-2022	Health	Mobile Health Van Donation for Safar Project	19,33,195
2021-2022	Health	Improvement in Health & Nutrition of Females	4,64,625
2021-2022	Health	Infrastructure Development at Primary Health Centre (PHC) Kharawar	14,76,847
2021-2022	Health	Safar – Risk Profiling of Truckers	16,26,000
2021-2022	Health	Safar Project for Truck Drivers	32,18,115
2021-2022	Health	Mobile Medical Unit Project	26,41,726
2021-2022	Health	Govt. Scheme Linkages	2,34,590
2022-2023	Health	Tarangini – (Maternal, Infant, Young Children, Female Adolescent Nutrition) Nutrition Project	43,39,386.00
2022-2023	Health	Risk Profiling Project for Truck Drivers	13,66,441.00
2022-2023	Health	Safar Programme for Truck Drivers	49,81,266.00
2022-2023	Health	Mobile Health Care Unit	31,87,738.00
2022-2023	Health	Eye Care Program	20,00,000.00
2022-2023	Health	Govt. Scheme Linkages - Health	4,80,000
2023-2024	Health	SAFAR - MMU for Truck Drivers	47,13,382.00
2023-2024	Health	SAFAR - Risk Profiling	18,91,600.00
2023-2024	Health	Tarangini – (Maternal, Infant, Young Children, Female Adolescent Nutrition) Nutrition Project	43,24,588.00
2023-2024	Health	Mobile Medical Unit Project	31,81,798.00
Total			84122594.00

2. CSR WORK UNDER WATER CONSERVATION AND RESOURCE DEVELOPMENT

Asian paints is doing water conservation and resource development program to address the water scarcity issue and promote water conservation nearby area under Corporate Social Responsibility.

Key Work done by Asian paints in area of water conservation and resource development program:

- a. Asian paints have done water conservation projects that benefited the communities around the factory area. These RHW project have helped in improvement of water quality along with conservation of good quality water. In some of institute where water logging was one of the major issue, significant reduction has happened after the implementation of urban roof top water harvesting projects. Below are the details of rain water harvesting project done in the surrounding area for the time period of 2021-2024.

RAIN WATER HARVESTING STRUCTURE

CSR Project Name- Rain water harvesting structure	Project Year	Implemented by (NGO/Vendor)	No of structure constructed	Rain water recharge potential)
Maintenance of existing Rainwater Harvesting structures in FDDI, MDU and B. D. Sharma institute (209 structures)	2021-22	D&D Ecotech, Mumbai (RWH Expert)	209	1896
RWH Maintenance - Rohtak 111 Nos (FDDI and PGIMS)	2022-23	FORCE NGO	111	7594
Total			310	135892

b. Water Pipe line connection to Kherisadh School:

The School is located near the plant and having strength of 420 children and 25 teachers. There was no direct water supply and school was fulfilling water requirement by procuring tanker water. Asian paints approached the HSIIDC for water connection and laid down the pipe line along with other infra for water by fulfilling all the HSIIDC requirement for water connection. Now school is getting good quality potable water supply throughout the year.

c. Water Pipe line connection to Kherisadh Village:

Kherisadh village with population of 5200 was facing the crisis of drinking water. Village main water supply pipeline had been blocked/damaged due to national highway work. There was no direct supply of water in village. Villages were forced to procure tanker water from private supplier at cost of 700 Rs per Tanker. In order to provide sustainable water solution to Kherisadh village, based on detail assessment of all possible intervention, the new pipe line of 2.4 km along the side of national highway laid down and connected with new borewell. By this project, about 3200 people from 650 households benefiting.

I. Rainwater Harvesting Projects by APL at Footwear Development & Design Institute, Rohtak:

Asian Paints has identified Water Conservation as a priority Corporate Social Responsibility area. For the Asian Paints unit in Rohtak, Haryana, it has been decided to identify Water Conservation projects that benefit communities around the unit location.

In this context, FORCE had conducted a Pre-Project Feasibility study to assess the options for Asian Paints. Based on the recommendations of the report, in year 2014-15, it was decided to focus on Rooftop Rainwater Harvesting in Institutions.

Based on the potential and feasibility keeping in mind budgetary and time considerations, 1 Govt institution had been identified and recommended for Rainwater Harvesting under 2014-15 of the Asian Paints CSR Program.

The detailed report on Rainwater Harvesting Project at Footwear Development & Design Institute, Rohtak, Haryana is provided as Report.

II. Rainwater Harvesting Projects by APL at School, Rohtak:



Project RWH Potential & Estimate

To	Mr. Sandeep Rao Iddya	Date	28th Feb'14
	Manager, EHS	Est. No	322/3
Client:	Asian Paints, Rohtak		
Project:	Rainwater Harvesting for school in Rohtak		

RWH Potential

Rooftop & Open Ground RWH via groundwater recharging

Sr. No	Description	Building	Open ground	Total
1	Area	2,000	11,000	13,000
2	Rohtak Avg. Rainfall (as per CGWB report. Copy attached)	515	515	
3	RWH Collection Co-Efficient	85%	20%	
	Total RWH Potential	8,75,500	11,33,000	20,08,500
	Average daily rainfall harvesting potential based on 25 days average	35,020	45,320	80,340
5	Rainfall expected at peak intensity i.e. 10 mm in 15 mins	17,000	22,000	39,000
6	Ideal holding capacity required for 70% of the rainfall expected at peak intensity in 15	11,900	15,400	27,300

Technical Notes :

Since the school faces water logging problems due to its ground being in a low lying area, we suggest the following

Roof Area

- 1 Channelling the rainwater collected on the roof via 4" PVC piping towards the Jal Rakshak recharge systems. This will help recharge the groundwater levels. Additionally it will help prevent flooding from the rooftop rainwater on the ground areas adjacent to the school building.
- 2 Creation of a trench in the low lying area to collect the rainwater falling on the ground.
- 3 Water from the trench will be diverted to the Jal Rakshak recharge systems for recharging the groundwater levels.
- 4 Rainwater from the left side of the school naturally flows into the right side of the school, where we are proposing trench. As such we do not need to create separate channelling for the same
- 5 We have suggested 6 Jal rakshak systems as per the calculations detailed above, keeping in mind the site conditions and need to remove water from the ground asap.



D&D Ecotech Services

35, 1st Floor, Raghuleela Mall, Palar, Kandivli (W), Mumbai - 400 087 Tel. 91-22-6725 3726 Email info@dnecotech.com Web www.dnecotech.com

d. Cleaning and Desilting work at Bohar Village Pond

The identified pond in Bohar village which was serving the purpose of cattle rearing and domestic utilities has become completely abandoned due to the spread of Water Hyacinth, an invasive species of water weed. The water weed when not controlled, cover the ponds entirely; this dramatically affects water flow and blocks sunlight from reaching native aquatic plants which often die. The decay processes deplete dissolved oxygen in the water. The plants also create a prime habitat for mosquitos.

The pond cleaning and desilting work was done. It would enable conservation of 9480 KL rainwater. It established a clean and healthy environment in community.

LAKE DESILTING PROJECT AT BOHAR VILLAGE, ROHTAK (JULY, 2020)



e. Irrigation Canal lining Brick Work:

Most of the channels existing in the region to carry irrigation water are unlined, and hence, a large part of irrigation water is lost in percolation and absorption as seepage loss. It accounts to be 25-50% of water lost due to seepage. It is a very serious loss and proportionately reduces the irrigation potential of the supplied water. Hence, there is need to reduce the seepage loss of the costly irrigation water. The seepage losses can be avoided or minimized by lining of irrigation channels.

The irrigation canal lining work completed in Kharawar Village to reduce conveyance loss of irrigation water by doing brick work on the irrigation channel. In 1st phase, total 680 meter brick work completed on irrigation channel.



Work done area of water resource development program in 2020-21:

In 2nd phase of canal lining work in Kharawar Village, total 587 meter long brick lining completed in Kharawar. Total 1267 meter canal line brick work completed in two phases.



Water Security: Under this *Watermark* theme, APL Rohtak carries out multiple interventions in the nearby villages for example Construction/Renovation of Canal Lining for efficient water usage in agricultural areas, Pond rejuvenation, Tree plantation, Sewage treatment through innovative solutions. Out of these interventions around Water conservation, Canal Lining is one of the flagship interventions of APL Rohtak Plant. Details of which are provided below:

The Canal Lining project under Watermark theme: Haryana is an agriculture intensive state and so is the district of Rohtak. Out of the total village population in and around Rohtak, 82-85% of population depends only on Agriculture. The irrigation water is supplied once in 40 days to these villages

through a network of unlined channels. The released water for the village does not reach on time because of losses in these unlined canals. The groundwater available in this area is brackish and is also expensive to draw.

Therefore, to address this issue, APL Rohtak plant has taken up an extensive intervention of Canal Lining, where the kuccha canals in the fields of local farmers are made pucca by providing proper lined channels for irrigation.

The objective of this intervention is as follows:

- Reducing the water loss due to percolation and absorption as a seepage loss.
- Reducing the maintenance cost of (desilting and removal of weeds) for farmers.
- Reduction in the annual utilization of ground water.
- Saving of fuel consumption in pumps for tube well due to reduced usage, saving money for farmers.
- Increase in yield (kg/acre) of crops using good quality river water than saline ground water, thus increasing the income of farmers to support their livelihood.



In the past few years, we have lined >9km length of irrigation canals and have planned another 6 km in the year 2024-25. Water savings from these lined canals over the years are shown below:

Year	Length of Canal lined (in meters)	Cultivable area to be irrigated through lined canals (in hectares)	Water conservation potential created (in KL)
2019-20	680	10.9	36515
2020-21	587	8.5	28475
2021-22	1,833	24.3	81405
2022-23	1,500	25.8	86430
2023-24	4,550	76.3	319590
Total	9,150	146	5,52,415

f. Trainings:

Total 12 no's of training program were arranged for the local farmer. The topic covered in training were vermicomposting, Technology-based cultivation, Soil health management, Preparation of organic formulation & improved irrigation methods

III. CSR Plan for upcoming 5 Years (2024-25 to 2028-29)

In the next 5 years, the company intends to continue to invest in community building CSR initiatives in similar trajectory and focus areas:

1. Health & Hygiene:

- Mobile Medical Unit
- Nutrition Centric Interventions
- Truckers Well-being Programme

2. Water Security:

- Construction/Renovation of Canal Lining for efficient water usage in agricultural areas
- Promotion of Water Use Efficiency
- Safe Drinking Water availability
- Grey water management
- Sewage treatment

3. Skill Development: Mobile Colour Academy

The Budget Allocation Projections for Next 5 Years:

Amount in crores.

Proposed tentative CSR Budget for APL Rohtak Plant						
Vertical	2023-24 (Actuals)	2024-25	2025-26	2026-27	2027-28	2028-29
Health & Hygiene**	1.42	1.16	1.20	1.20	1.20	1.20
Watermark**	2.81	3.95	4.00	4.25	4.50	4.75
Total*	4.23	5.11	5.20	5.45	5.70	5.95

Budget projections is subject to change basis overall CSR mandate and location Specific allocation.

***CSR Operations under Health & Hygiene and Water Security will be carried out in 20 km periphery of Rohtak manufacturing facility.*

Apart from this, we will continue with our Pan India Skilling initiatives via Mobile Colour Academy across the state of Haryana with a budget of ~1 crore planned in the state.

Annexure -9

At Asian paints Rohtak plant we have taken below steps for Sensitization of employees and implementation of ban on Single Use Plastic (SUP) –

1. Circulation of emailers to all employees regarding the ban on single use plastic along with the item's details:

Single-Use Plastic Ban in the Premises



Kumari Anubhuti

To: Rohtak Managers; Rohtak Executives; Rohtak Team Members

Cc: Godwin Kumar Joti; Aditya Sinha; ANAND OSWAL; Vishal Kumar Varshney; Amardeep Jain

You forwarded this message on 7/14/2022 12:22 AM.
This message was sent with High importance.

Reply Reply All Forward

Sat 7/2/2022 12:35 PM

Hello All,

In adherence to the **Single-Use Plastic Ban** in Haryana, Please find the following list of items, usage of which is to be **banned immediately** in the plant premises.

S. No.	Items	Plant - Usage	Remarks
1	Candy Sticks	NA	
2	Ice-Cream Sticks	NA	
3	Plastic Straw	Used in Juice-boxes, usage stopping immediately	
4	Plastic Stirrer/Earbuds	NA	

11	Polystyrene/ Thermocol for decoration	NA	
12	Plastic Carry Bags	Respective departments to ensure compliance	
13	Plastic Sheets <75µm till 31st Dec 22 after that 120 µm	Respective departments to ensure compliance with the vendors	Please ensure the same requirement is also mentioned in the next PO.

Please note these items are banned for personal use as well. Please **DO NOT** bring these items inside the premises in any case, even for personal use.

In case of clarity needed for usage of any item, please get in touch with the EHS team immediately.

Regards,

Anubhuti

2. Add clause on restricting single use plastic in purchase orders.

FW: Single-Use Plastic Ban in the Premises



Kumar Anubhuti

To: Aashu Gupta Sunny Chandra

Cc: Bhupender Singh

This message was sent with High Importance.

Reply

Reply All

Forward

Sat 26 Aug 2022, 09:02 AM

Classification: Internal

Hi Aashu,

As discussed yesterday on call, Please find the following notification for the single use plastic ban.

Request you to please mention point no. 10 (PVC Banners < 100 μ m) and point no. 13 (Plastic Sheets < 75 μ m till 31st Dec 22 after that 120 μ m) in the list of requirements/pre-requisite while getting a P.O.


Please initiate/do the needful on priority.



Regards,

Anubhuti

This message has been classified Internal by Kumar Anubhuti on 06 August 2022 at 06:01:40.

3. Awareness created through mailers for all employees.

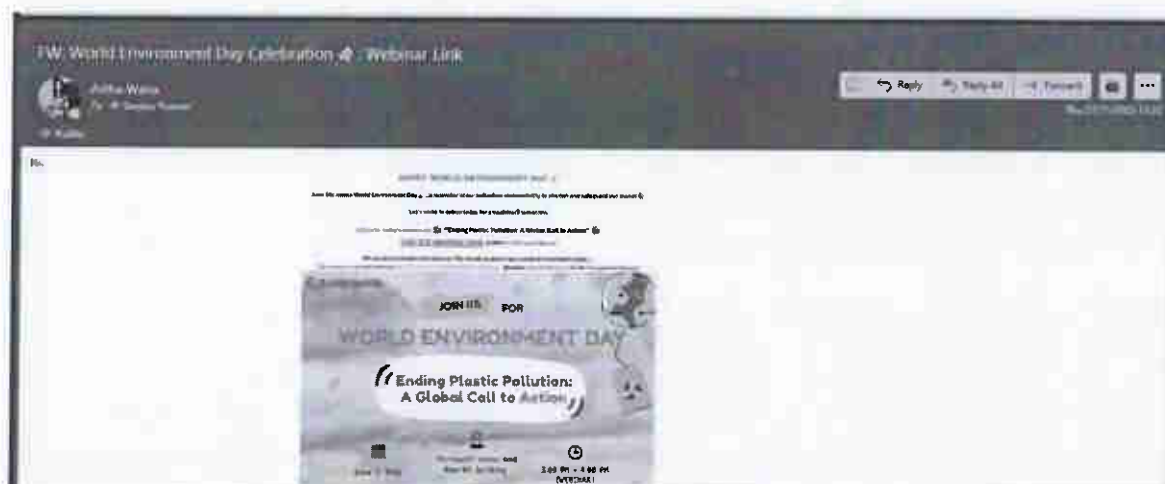

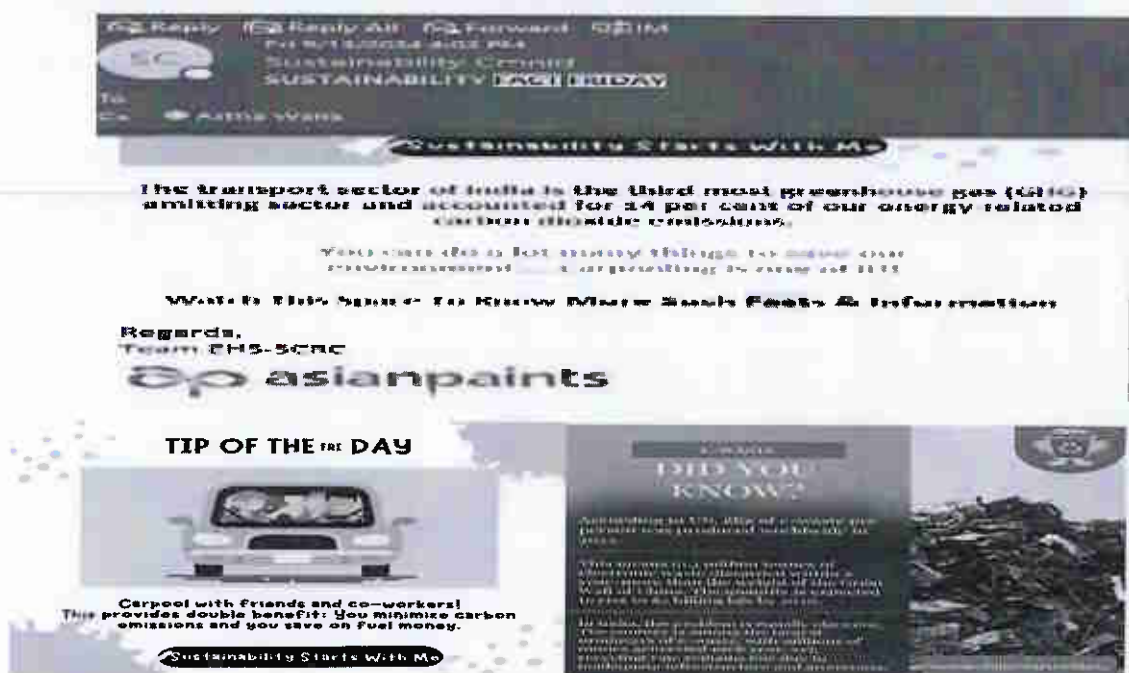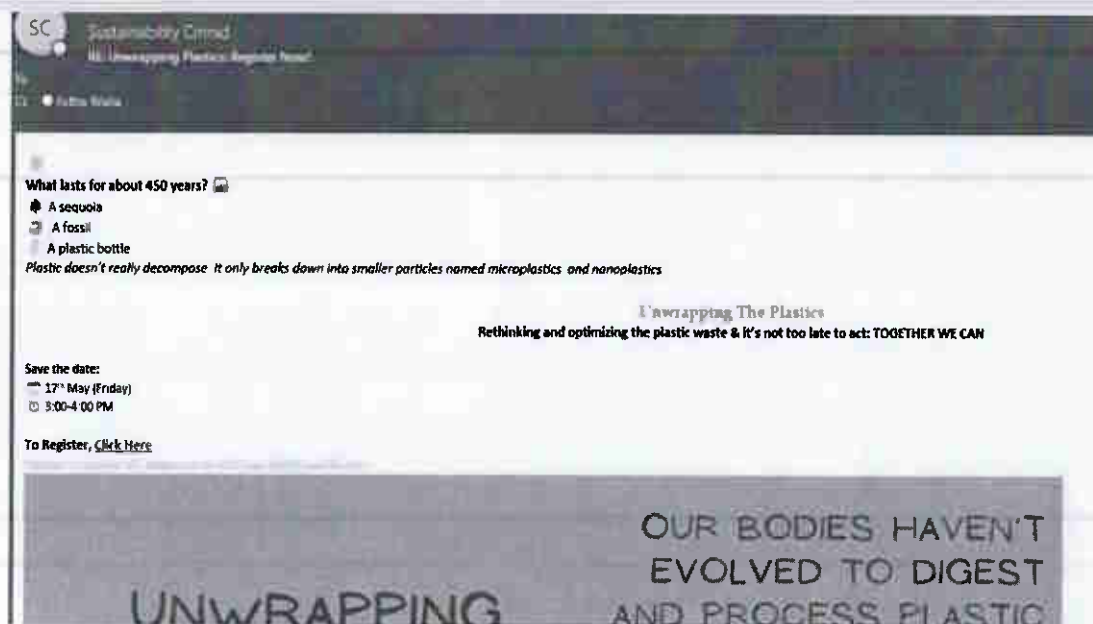

4. Environment Week Celebration inside the plant





5. Plastic Wrapping has been removed from packing material packaging.

